
School District of Volusia County Project Oversight Committee Report

Fiscal Year Ending June 30, 2003



School Board of Volusia County

Mrs. Vicki Bumpus, Chairman Mr. Earl C. McCrary, Vice Chairman Ms. Judy L. Andersen Ms. Judy Conte Ms. Candace Lankford

Superintendent of Schools Mr. William E. Hall

Through the individual commitment of all, our students will graduate with the knowledge, skills, and values necessary to be successful contributors to our democratic society.

<u>Volusia County School District</u> <u>Project Oversight Committee Report</u> <u>Fiscal Year ending June 30, 2003</u>

The School Board of Volusia County, Florida

Project Oversight Committee Members - June 30, 2003

Ms. Garrette Covington, Management Consultant Covington & Associates, Inc., Daytona Beach, Florida Term ends: December 31, 2004

Mr. Thomas Ewart, Retired Architect Retired School Administrator, Deltona, Florida Term ends: December 31, 2004

Mr. Jeffrey Malmborg, President Jeff Malmborg Construction Co., Inc., DeLand, Florida Term ends: December 31, 2006

Mr. Leonard Marinaccio III, Chief Financial Officer Bomar Construction, Inc., Ormond Beach, Florida Term ends: December 31, 2006

Mr. Kenneth Parker, City Manager City of Port Orange, Port Orange, Florida Term ends: December 31, 2004

Mr. Adelson Ramos, President Architectural Animation and Design, Inc., Ormond Beach, Florida Term ends: December 31, 2006

Mr. William C. Kelly, Jr., Assistant Superintendent for Financial Services Volusia County School District, DeLand, Florida Term ends: At Will

Project Oversight Committee's Meeting Schedule

- October 29, 2002, Campbell Middle School, 3:00 PM
- December 13, 2002, DeLand Administration, 1:00 PM
- March 7, 2003, Facilities Services Building, 3:00 PM
- March 19, 2003, Facilities Services Building, 3:00 PM
- April 16, 2003, DeLand High School, 3:00 PM
- May 21, 2003, Facilities Services Building, 3:00 PM
- June 26, 2003, Facilities Services Building, 1:30 PM
- July 9, 2003, Facilities Services Building, 1:30 PM

Table of Contents

Description	Page No.
Introduction	4
Revenues and Debt Management Tools	5
Expenditures	7
Schedule Revisions	8
Progress/Status	14
Implementation of Prior Year Recommendations	15
Recommendations	17
Conclusion	19
Report of Sales Tax Collections – Actual to Original Projections	21
Report of Sales Tax Sources and Uses	22

Ten Year Construction Schedule	23
Project Status Report	27
Project Status Report – Changes in Scope	32

Project Oversight Committee Report June 30, 2003

INTRODUCTION

On October 9, 2001, the voters of Volusia County approved a referendum adopting a half-cent sales tax (the Referendum) for fifteen years, effective January 1, 2002, to fund the Volusia School District Board (the School Board) approved ten-year plan to construct certain identified educational facilities. The Referendum placed before the voters established a Project Oversight Committee (the Committee). The Committee was charged with the responsibility of reporting on the implementation, progress, status and completion of the sales tax construction projects listed within 90 days of the end of each fiscal year. The Committee was established in the Referendum to provide additional assurance to the citizens that the School Board is meeting its commitments and obligations related to improvements promised during the 2001 election.

This is the second annual report of the Committee and is being filed consistent with the requirements of the Referendum. Because of the requirement to submit a report within 90 days after the end of the fiscal year of the School District of Volusia County (The School District), this report covers the first two fiscal years of activity ending June 30, 2003.

Included in this report is information regarding current status of projects funded by sales tax including changes in scope as well as timeline fluctuations. The report also encompasses progress made on prior year recommendations.

REVENUES AND DEBT MANAGEMENT TOOLS

(See Report of Sales Tax Collections – Actual to Original Projections, page 21)

The School Board staff estimated sales tax collections from January 1, 2002 through June 30, 2003 to be \$28,799,237.42. The actual sales taxes collected during this period were \$38,123,922.80. The excess of actual over projected collections was \$9,324,685.38, approximately 32% over projections. Collections recognized in this fiscal year total \$27,917,430, with the School District's financial statements for the fiscal year ended June 30, 2003, report \$29,497,203 in sales tax revenues; the difference is attributable to accruals for April, May, and June 2003 revenues. Investment earnings on sales tax collections and bond proceeds through June 30, 2003 were \$2,413,540.

While the District continues to see a trend of increased collections in the second year, there are no assurances that this trend will continue in future years. Any collections that exceed projections will be added to the amounts set aside for contingencies. In addition to meeting unforeseen costs on projects, these funds will be used for site acquisition and site improvements on listed sales tax projects. Any amendment to the adopted project list will require legal notice and a public hearing before the School Board prior to any action by the board.

In order to take advantage of the historically low interest rate environment, the School Board entered into an interest rate swap agreement with Salomon Brothers Holding Company, Inc. ("SBH"), expressed as a Fixed Spread Project Oversight Committee Report June 30, 2003

Basis Swap. The School Board entered into this agreement as a tool to manage interest costs associated with the Series 2002 Sales Tax Revenue Bonds. The agreement provides that the district will make payments at a variable rate based on the Bond Market Associate Municipal Swap Index ("BMA") less a fixed spread to SBH, and SBH will make payments at a variable rate based on USD Libor-BBA (Libor) to the District. At June 30, 2003, the termination value of this swap agreement is \$(589,000) and the accrued benefit is approximately \$23,800 for the period from inception of the transaction in March.

District staff report that the termination value of the swap will vary as (i) interest rates increase and decrease and (ii) the relationship between taxable and tax-exempt interest rates changes. In the current environment of historically low interest rates and historically high relationship between tax-exempt and taxable securities, the termination value is negative. However, even a modest increase in long term interest rates will move the termination value in the District's favor.

The District does not intend to terminate the swap, much like a long-term investment, so positive or negative changes in termination value are not material. The primary purpose of the transaction is to reduce net debt service payments as has occurred during the first three months.

The School Board approved a resolution in late June, to allow the Board to enter into an agreement with a financial institution for a Line of Credit. This will allow the School Board to finance certain educational facilities, without the issuance of additional debt. This is another debt management tool used Project Oversight Committee Report June 30, 2003

to minimize interest expense, while continuing to provide the district a vehicle to enter into construction contracts and encumber the needed funds.

EXPENDITURES

(See Report of Sales Tax Sources and Uses, page 22)

During the period ending June 30, 2003, the School District expended \$26,032,006, including \$7,628,958 in debt service costs of sales tax funds. As noted later in this report, the reuse of plans, as well as the current construction-bidding environment has provided the District with opportunities to construct schools at a lower cost than four years ago. Land acquisition and off-site improvements on sales tax projects have been funded using contingency funds. The District anticipates utilizing sales tax funds for land acquisitions and off-site improvements for Elementary Y, Elementary V, Elementary Z and High School DDD or other projects where a site is not already owned.

The District paid \$7,628,958 in interest expense on the Series 2002 Sales Tax Revenue Bonds during fiscal year 2003. In fiscal year 2004, the debt service expense will be \$14,358,607.50, including \$8,020,000 in principal payments.

As of June 30, 2003, the School District has \$151,980,334 available in sales tax funds for construction projects.

SCHEDULE REVISIONS

(See Ten Year Construction Schedule, page 23)

The fiscal year 2002-03 witnessed substantial and visible gains in the 10year construction program as months of planning came to realization through contracts and subsequent construction. T.T. Small Elementary, Daytona Beach addition was completed in February. Campbell Middle School, Daytona Beach is nearing completion and will be ready for occupancy this fall. Seabreeze High School, Daytona Beach, Phase III is complete and DeLand High, DeLand, Phase III is well underway. The groundbreaking for the new Mainland High School in Daytona Beach was April 30, 2003 and the construction progress is highly visible to the public, along International Speedway Boulevard in Daytona Beach.

Once earthwork begins on Middle "GG", Daytona Beach, located on Clyde Morris Boulevard, another segment of the general public will see the impact of their support of the half-cent sales tax. Other projects making substantial progress, but less visible, are Elementary "W" in Deltona and the addition to Volusia Pines Elementary, Lake Helen. Site plan issues have been resolved in New Smyrna Beach, Orange City and Pierson to allow other construction projects in those jurisdictions to proceed. Two possible sites have been identified and are under option for new High School "DDD", one in DeBary and one in Orange City, with a decision expected in August.

The time needed for advertising the bids, awarding of bids by the board, and execution of contracts (approximately three months) is incorporated in "Planning." The time allotment for receiving and installing furniture and equipment and actual move-in is incorporated into the "construction" portion of the schedule. This can require from six weeks to three months depending on school size.

New Smyrna Beach High School, New Smyrna Beach - anticipated completion date has been rescheduled from October to December 2005. The schedule was amended to allow modifications in the plans at staff members' requests and for permitting. Construction is scheduled to begin in September 2003.

DeLand High School, DeLand – Phase III construction began on the auditorium building as projected in August 2002. Planning difficulties continued throughout the year and construction began on the renovations of the older classroom buildings in February 2003. Completion is projected for December 2004 for all construction.

Mainland High School, Daytona Beach – construction began in May, two months later than originally projected; however, the project is still on schedule for the original completion date of May 2005.

Campbell Middle, Daytona Beach – construction began as projected. Completion is scheduled for August 2003 with occupancy occurring in the fall. Demolition of the remaining buildings and redevelopment of the site are to follow with completion projected for spring 2004.

T.D. Taylor Middle/ High, Pierson - Construction is now scheduled to begin in January 2004. Site issues, as well as reconciling budget and design have

affected the planning schedule. Completion of the entire project is projected for May 2006.

Middle School "GG, Daytona Beach – the construction schedule was affected by bidding complications, which necessitated a re-bid. The contract completion date is scheduled for December 2004 with occupancy to follow. This is six months earlier than original projection.

Elementary "X", Orange City – construction is scheduled to begin in September 2003 with completion in fall 2004 and occupancy to follow. The schedule has been affected by complications in utility design and acquiring sanitary sewer line easements.

Elementary "W", Deltona – construction began in May 2003. Construction completion and occupancy remain scheduled for summer 2004.

Deltona High School heating, ventilation and air conditioning (HVAC) project, Deltona – construction began in June 2003, six months later than originally projected due to the complexity of planning issues. It is scheduled for completion in January 2005. The project includes replacement of the HVAC system school-wide. Only a portion of this project is funded by sales tax, the balance is funded through other district funds.

Chisholm Elementary School, New Smyrna Beach – renovation to buildings 8 and 9 has been completed. The balance of the campus will be addressed in phases to accommodate the school calendar. Completion is scheduled for December 2004.

Volusia Pines Elementary School, Lake Helen – construction began in January 2003, three months ahead of schedule. Completion is projected for October 2003.

Tomoka Elementary School, Ormond Beach – construction has been rescheduled from February 2003 to begin in November 2003 due to planning issues. Completion is now scheduled for August 2004.

High School "DDD", Southwest Volusia – this project has been accelerated in response to overcrowding at three southwest high schools. Deltona High, Pine Ridge High School, both located in Deltona, and DeLand High School DeLand have approximately 1,500 students combined, over capacity. This is a high growth area and it was determined that High School "DDD" was a priority.

Site search is in progress with two sites under option by the board with a decision planned in August 2003. Planning is scheduled to begin in October 2003 with construction beginning, at the earliest, in April 2005 for a completion date of June 2007. This schedule may be revisited, as the site issues are more clearly defined.

Southwestern Middle School, DeLand – the site improvements have been completed. The renovation project that includes air conditioning the gym, converting a classroom to a technology lab and electrical upgrades are in planning. Defining the scope of the project in combination with the federal grant for ADA compliance has been challenging. Construction is scheduled for completion March 2005. *Blue Lake Elementary School, DeLand* – the ceiling and lighting replacement project has been rescheduled for March 2004 to avoid conflict with projects funded by other district funds. Once that construction is concluded, the ceiling and lights will proceed in June 2004.

Bonner Elementary, Daytona Beach - HVAC project installation has been rescheduled for summer 2004 for school schedule coordination purposes.

Alternative Education for SW Volusia – the Daytona Beach Community College, Highbanks Facility, in DeBary has been selected as the site for alternative education in the southwest. This property was scheduled to close by June 30, 2003, with minor renovations in fall 2003. As of the date of this report, the sale of property has not closed. It should be ready for occupancy by January 2004, two years ahead of schedule.

Coronado Elementary School, New Smyrna Beach – the upgrade of electric and air conditioning replacement has been rescheduled to coordinate with another district-funded project on campus. Construction should begin in May 2004.

Galaxy Middle School, Deltona – the science classroom improvements have been rescheduled for construction summer of 2004 from summer 2003. This was for planning purposes.

Project Oversight Committee Report June 30, 2003

Read–Pattillo Elementary School, New Smyrna Beach – the replacement of windows and doors has been rescheduled from May 2003 until May 2004 for planning purposes.

Sunrise Elementary School, Deltona – the extension and connection with central sanitary sewer has been rescheduled for planning in January 2004 with construction beginning in January 2005. This is one year later than original schedule but should coincide with other work being performed on the utility system in the area.

Holly Hill Middle School, Holly Hill – the schedule for replacement of Holly Hill Middle has been revised from June 2003 to have planning begin in May 2004. This project was rescheduled to coincide with anticipated revenue availability due to the acceleration of new High School "DDD."

Alternative Education for Southeast Volusia – the project schedule has been revised to begin summer 2004 from August 2003 for planning purposes. The acquisition of the SW Alternative Education property will be the focus for meeting the needs of Alternative Education this coming fiscal year.

Hurst Elementary School, Holly Hill – the replacement of Hurst Elementary was deferred for one year due to anticipated revenue availability. This schedule change is also in response to the acceleration of High School "DDD."

The balance of the schedule remains essentially unchanged. Many of the revisions were in response to conditions outside the control of the School

Board, such as permitting by outside agencies and are typical in construction projects of this nature. The original schedule is used as a planning and tracking tool and is changed to accommodate changing priorities and development challenges. The program remains well on track for completion by 2011.

PROGRESS/STATUS

(See Project Status Report, page 27 and Changes in Scope, page 32)

In the second year of the 10-year program, substantial and visible progress has been made as evidenced by the attached report. Over \$100 million in construction contracts have been awarded this fiscal year. An additional \$8 million has been completed with the conclusion of the final site work at Seabreeze high School in Daytona Beach. The accompanying report is more detailed as to activities at each site.

The highlights of the year were the completion of Seabreeze High School Phase III, Daytona Beach; the beginning of construction at Mainland High School, Daytona Beach; construction starts at Volusia Pines Elementary, Lake Helen; Elementary "W" in Deltona; completion of T.T. Small Elementary, Daytona Beach addition; near completion of Campbell Middle, Daytona Beach and beginning the auditorium and renovation portion of DeLand High School's Phase III.

Plans for construction of Elementary "X" in Orange City and the replacement for New Smyrna Beach High School in New Smyrna Beach

Project Oversight Committee Report June 30, 2003

have been finalized and were advertised for bid in June 2003. The bidding climate continues to result in favorable bids for the district.

The committee held meetings at Campbell Middle School in Daytona Beach and DeLand High School in DeLand this year. These meetings included a tour of the construction site and discussions with the district's project manager and other job personnel. The committee received information related to specific program and construction decisions as well as observation of the quality of the work. Next year will include more site visits as construction progresses. The committee was favorably impressed with the technical knowledge of the staff and the quality of workmanship on each job.

In addition to major construction projects listed above, 21 of 44 schools now have new playground equipment for both intermediate and primary age students.

IMPLEMENTATION OF PRIOR YEAR RECOMMENDATIONS

The District has developed a public information program to provide the citizens of Volusia County with information about the status of the sales tax construction projects, as well as provide an opportunity for input. The District has followed up on last year's recommendation in several ways.

 Speaker's Bureau – Several District representatives, including Mr. Bill Kelly, Assistant Superintendent for Financial Services, Ms.
 Patricia Drago, Executive Director of Facilities and Mr. Tom Besaw, Coordinator of Career and Technical Education, have given presentations to several organizations including DeLand Business Partners, Career Connection, Daytona Beach Chamber of Commerce, Leadership DeLand, Ormond Beach Rotary, Volusia Manufacturer's Association, District Advisory Council, Teachers' Advisory Council and several schools' School Advisory Councils.

- Both Mr. Kelly and Ms. Drago have appeared on television with Spotlight on Volusia County Schools, Volusia County Administration and other local television shows taped for Station WCEU-15.
- Ms. Drago provided an update regarding sales tax funded projects on WNDB Radio Station and Mr. Kelly has interviewed with Mr. Bill Schuman, a radio news broadcaster.
- Several joint meetings held with the School Board and local cities have addressed sales tax project issues, including the impact on infrastructure and surrounding areas, relative to individual projects.
- Ms. Saralee Morrissey and Ms. Drago appeared before local government planning agencies and elected officials on numerous occasions during the planning process.
- The School Board continues to maintain and improve a website dedicated to the half-cent sales tax. The website address is www.volusia.k12.fl.us/CustomerService/half_cent_sales_tax.htm
- Signage is being developed that will be placed at each school site benefiting from sales tax funds, identifying the project as a sales tax funded project.

Both Middle "GG" and Elementary "W" will be used for benchmarking against their predecessor's prior construction costs and measured against schools under construction by other districts. The criteria will be price, quality, effectiveness and efficiency. Because both schools are a re-use of plans, detailed inflationary costs and cost of delivery method will be available. After occupancy of a new facility, the occupants will be surveyed for their opinion as to efficiency and productivity. These will be included as a measure of effectiveness.

RECOMMENDATIONS

The committee recommends to the School Board that it continue to exercise caution in anticipating that sales tax collections exceed original projections. Every indicator shows that original projections were very conservative; however, it is premature to expand the project list or scope of current projects.

The School Board has benefited from a very competitive constructionbidding climate as evidenced by the construction bids for Middle "GG" located in Daytona Beach and Elementary "W" located in Deltona. Both of these projects are reuse designs from prior schools with little modification. The bid for Elementary "W" is \$313,414 less than the cost to construct this school in 1999. Middle "GG" is \$1,514,800 million less than the cost of construction in 1999. The committee urges the district to continue to take advantage of the current construction bidding climate to the extent possible because the savings realized today may be needed to offset increased costs in the future.

The committee recognizes that some of the renovation and replacement projects appear to be running over projected budgets. While this may be typical of renovations, the committee wishes to caution the School Board regarding scope changes that increase the budget and use of contingency funds for items not originally within the project scope.

The committee also urged caution regarding any revisions in schedule. We are concerned that over time, projects to meet the needs of growth could result in the delays in replacement and renovation projects. The committee is convinced that many voters supported projects to improve existing school conditions. The committee is very concerned that facility needs in all areas of the county be equitably addressed, both growth and replacement.

The committee expressed its concern regarding the impact of the Class Size Reduction constitutional amendment and the enabling legislation on the tenyear building program. The committee encourages the School Board to keep Volusia County citizens informed about the impact Class Size Reduction will have on the stated goal of reducing portable classrooms by 70%. It was also recognized that the prototype plans for elementary and middle schools will need to be revised in recognition of more, smaller classrooms. New High School "DDD" and New Elementary "V" will probably be the first schools designed to meet Class Size Reduction criteria.

The committee recommends that the School Board inform the Governor, Legislature and Florida Department of Education of the impact that the Class Size Reduction amendment will have on achieving the objectives of the Sales Tax Referendum. In addition to the impact on educational services delivery, the stated goal of reducing portables by 70% seems unattainable with the addition of classrooms needed to implement for Class Size Reduction.

CONCLUSION

The Project Oversight Committee was established to provide additional assurance to the citizens that the School Board is meeting its commitments and obligations related to improvements promised during the 2001 election. The Referendum charges the Committee with the responsibility of reporting on the implementation, progress, status and completion of the sales tax construction projects listed. The Project Oversight Committee held seven public meetings during the 2003 fiscal year. The meetings held continue to acclimate the committee members to the District's policies and procedures, develop an effective monitoring process, as well as complete an annual report on the District's implementation, progress, status and completion of sales tax projects. Notes were kept of each meeting. The meetings were held at various locations, including recently completed project sites to provide committee members with first-hand experience of the School Board's construction product.

The \$103 million in construction projects contracts awarded this fiscal year has had a significant impact on Volusia's economy. Although there is no requirement for local participation, a review of the list of subcontractors on current projects indicates that local subcontractors who employ residents of Volusia County perform approximately 70% of the work. The building program provides a dual benefit, the taxpayers receive the benefit of improved educational facilities for our children and provides stimulus to the local economy and job market. The Committee commends the District staff for their responsiveness and the clarity and quality of materials presented to the Committee. The Committee is impressed with the manner in which the Facilities Division has handled the additional workload of such an ambitious building program with only minor changes in staffing. The quality of planning and depth of the organizational commitment of the Division is apparent in how smoothly the projects are progressing. The Facilities leadership team has repeatedly demonstrated the ability and willingness to adapt to the changing circumstances they face. We have also been impressed with their knowledge of the county and the thoughtful consideration given to the varying needs and goals of the diverse communities impacted by the construction projects in their neighborhoods.

Based on the facts and information provided by the School Board, the onsite observation of construction sites, and of district personnel the Committee was able to reach a conclusion on the progress of the half-cent sales tax tenyear construction program. The level of accomplishment observed in the second year of the building program reinforces the confidence the committee has that the School Board is making the progress necessary to meet the tenyear construction schedule approved by the Board and the Committee has confidence in the ability of the District staff to complete the construction program.

SCHOOL DISTRICT OF VOLUSIA COUNTY

Project Oversight Report Sales Tax Collections - Actual to Original Projections June 30, 2003


	Actual Collections	Projected Collections	Difference	Date Received
January	\$ 2,414,115.67	\$ 2,034,989.93	\$ 379,125.74	April 2002
February	2,508,746.13	1,702,991.94	805,754.19	April 2002
March	3,199,653.67	2,152,945.79	1,046,707.88	May 2002
April	2,083,977.75	2,161,774.08	(77,796.33)	June 2002
May	2,173,344.14	1,916,682.74	256,661.40	July 2002
June	2,683,416.71	1,884,204.30	799,212.41	August 2002
Subtotal	15,063,254.07	# 11,853,588.78	3,209,665.29	FYE 2002
July	2,499,681.19	1,901,635.64	598,045.55	September 2002
August	2,202,297.14	1,768,109.96	434,187.18	October 2002
September	2,624,607.55	1,827,627.47	796,980.08	November 2002
October	2,160,820.51	1,731,356.71	429,463.80	December 2002
November	2,162,309.09	1,768,109.96	394,199.13	January 2003
December	3,053,310.98	1,793,002.96	1,260,308.02	February 2003
January	2,740,721.19	2,145,366.82	595,354.37	March 2003
February	2,681,363.40	1,773,277.18	908,086.22	May 2003
March	2,935,557.68	2,237,161.93	698,395.75	June 2003
Subtotal	23,060,668.73	# 16,945,648.64	6,115,020.09	FYE 2003
Total	\$ 38,123,922.80	\$ 28,799,237.42	\$ 9,324,685.38	

SCHOOL DISTRICT OF VOLUSIA COUNTY


Project Oversight Report Sales Tax Sources and Uses June 30, 2003

Sources	Current Year	Prior Year	Total
Sales Tax Collections	\$ 27,917,430	\$ 10,206,493	\$ 38,123,923
Bond Proceeds	-	150,344,068	150,344,068
Unrestricted Interest	2,413,540	979,796	3,393,336
Restricted Interest	47,588	20,041	67,629
Total Sources	30,378,558	161,550,398	191,928,956
Less: Uses			
Land Acquisition and Site Improvements	4,498,957	3,324,077	7,823,034
Design Services	4,845,667	877,920	5,723,587
Construction Services	7,012,034	1,188,001	8,200,035
Furniture, Fixtures and Equipment	440,777	-	440,777
Facilities Management	1,605,613	514,007	2,119,620
Debt Service	7,628,958	· _	7,628,958
Total Uses	26,032,006	5,904,005	31,936,011
	<u> </u>	@155 (AC 202	\$150 000 045
Excess (Deficit) of Sources over Uses	\$ 4,346,552	\$155,646,393	\$159,992,945
Fund Balances			
Reserved for Debt Service			8,012,611
Tunnan			151 000 224


Unreserved Total Fund Balances 8,012,611 151,980,334 \$159,992,945

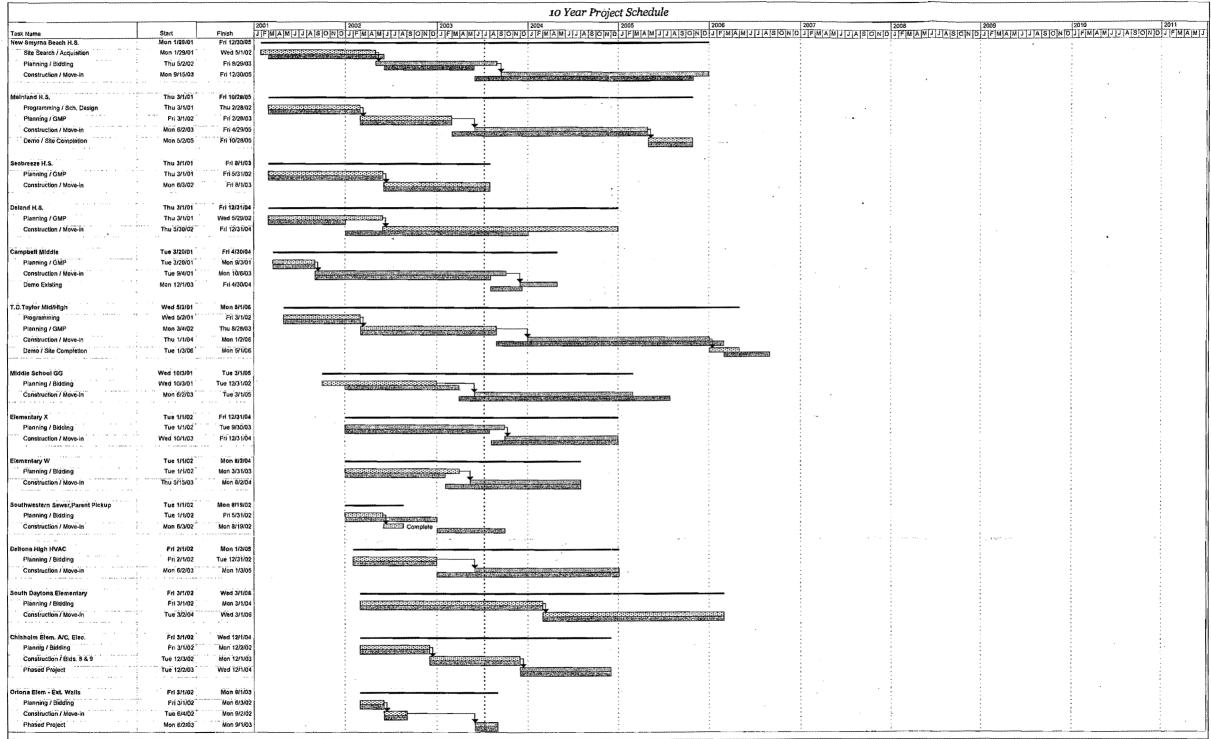

Page 1

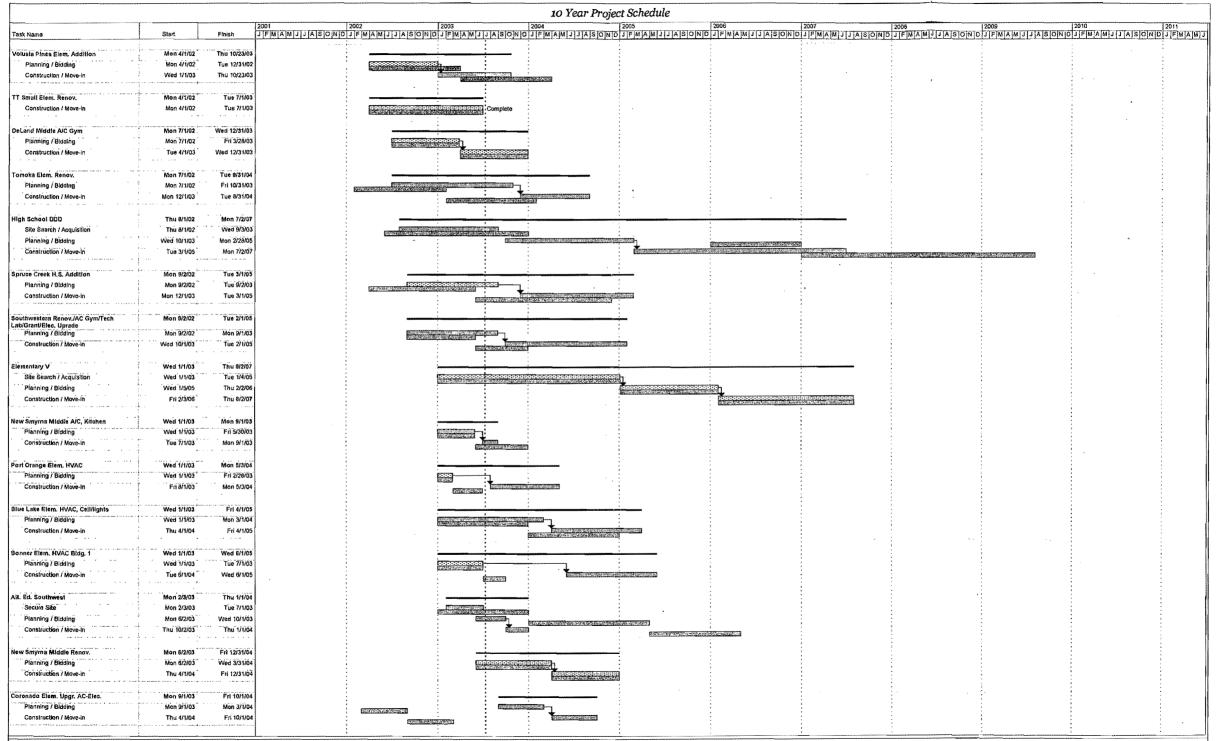

10YrProjSchd(itshotinhere2).mpp 6/11/2003 Page 2

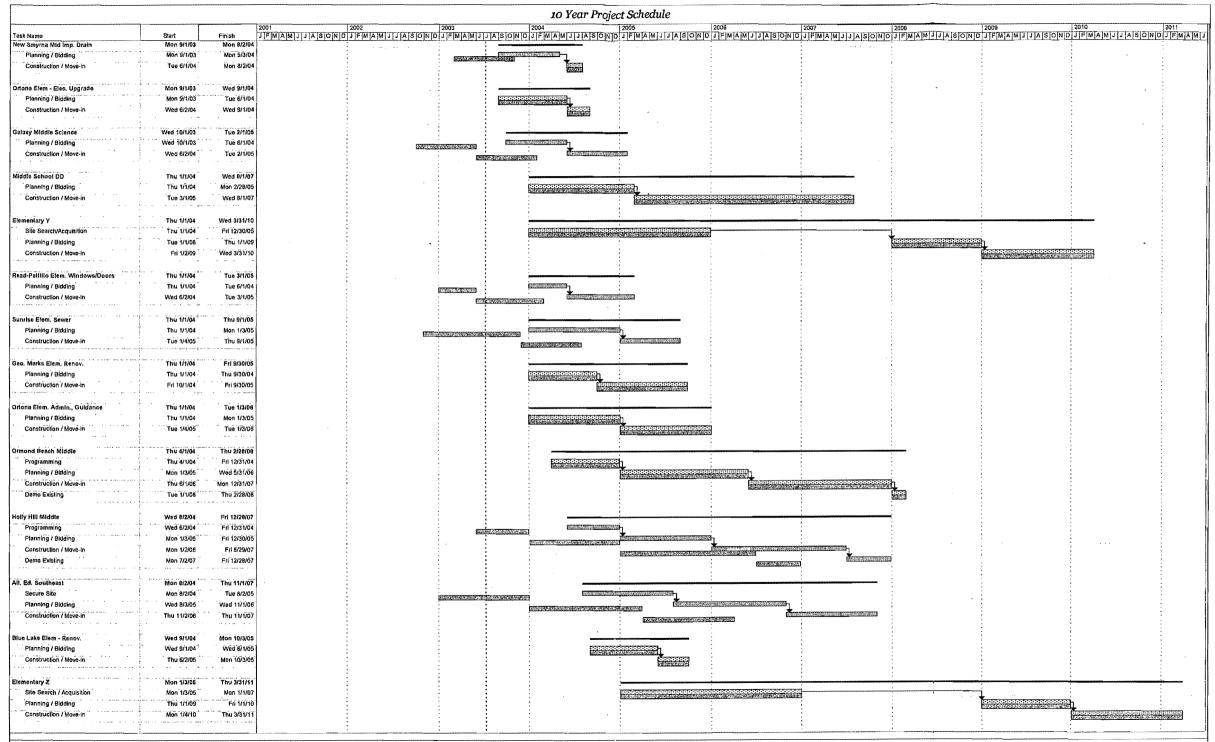

10YrProjSchd(itsholinhere2).mpp 6/11/2003

Page 3

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 ASSUMPTIONS AND EXPLANATIONS

ORIGINAL REPORT: The initial report dated January 29, 2001 utilized for Board approval (March 20, 2001) of this report's sales tax projects.

PROJECT: A unique location where construction and or renovations take place.

<u>NAME</u>: The actual location of the project's construction and or renovation. In some cases the project location is not currently known, however, when finalized the project name will be assigned. No names have changed since the ORIGINAL REPORT.

DESCRIPTION: A brief explanation of the construction or renovation to be performed on a project. Descriptions may change from report to report to best reflect changes to a project's scope. No descriptions have changed since the ORIGINAL REPORT.

MOST RECENT ESTIMATE: The best current estimate of a project's cost.

ORIGINAL PROJECT ESTIMATE: The initial cost estimate assigned to a project reflected on the ORIGINAL REPORT. Includes hard cost, fees and furniture, fixtures and equipment. Excludes site acquisition, permitting, off site cost and enhanced hurricane protection area. The ORIGINAL REPORT showed total construction cost of \$392,964,412.

<u>CHANGES IN SCOPE:</u> Increases or decreases (from ORIGINAL PROJECT ESTIMATE) in the cost of a project due to changes in the amount of work to be done. Items may also include those excluded in the ORIGINAL PROJECT ESTIMATE. Scope items may be funded from sales tax or non-sales tax funds.

<u>CONTINGENCY</u>: Costs added to or subtracted from a project resulting from unforeseen causes. A provision of \$33,035,588 was assigned to all projects in the ORIGINAL REPORT. As contingency amounts are determined, they will be reflected in this column.

INFLATION: Inflation results from timing differences between the initial estimate made as of January 29, 2001 (ORIGINAL REPORT) and November 30, 2002 (this report). A rate of 4% per year was assumed in the ORIGINAL REPORT totaling \$28,274,038 for inflation and \$60,725,962 for interest on debt for all projects. As inflation amounts are determined, they will be reflected in this column.

TOTAL: The sum of ORIGINAL PROJECT ESTIMATE, CHANGES IN SCOPE, CONTINGENCY and INFLATION. This sum represents the total cost of a project.

(NON-SALES TAX) OTHER FUNDS: Funds (future or current) used for a project's construction and or renovation derived from sources other than sales tax. The ORIGINAL REPORT assumed that \$54,000,000 in non-sales funds could be found for all projects.

TOTAL SALES TAX FUNDS: The amount of sales tax funds utilized in a project. The ORIGINAL REPORT estimated that a total of \$461,000,000 in sales tax funds would to used for all projects.

TOTAL COST TO DATE: The total of all expenditures and encumbrances of a project's estimated cost.

<u>UNCOMMITTED</u>: A project's estimated cost not contracted.

COMMENTS / NOTES: Explanation of material items related to a project.

.

				2001 2002	2003	2004	2005	2006 2007	20	08	2009	2010 20
			Start Finish	JFMAMJJASONDJFMAM	JJASONDJFMAMJJAS	ONDJFMAMJJASOND	JFMAMJJASONC	JFMAMJJASONDJFMA	MJJASONDJ	FMAMJJASONC	JFMAMJJASOND	JFMAMJJASONDJ
amage data by bar in the over intervent intervent in the over intervent in the over intervent int				:							+ +	
											-	-
		Construction / Move-in	Tue 4/4/06 Fri 6/1/07	1 4					(555) 通路		•	1 · · ·
		1				4			:			
demonstrations Number of N	Generation Market Market	lerson Elem. Renov.	Mon 1/3/05 Fri 12/29/06									
demonstrations Number of N	Generation Market Market	Planning / Bidding	Mon 1/3/05 Fri 12/30/05	, 1		3		h :	:			
							CONTRACTOR DEPENDENCE OF A PRODUCT OF A PROPERTY OF A PROP	Construction of the second state of the second	1			
Subal Parts II No. 1021 Pilotopic III No. 1021 Pilotopic IIII Pilotopic IIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIII				f					•		•	
Subal Parts II No. 1021 Pilotopic III No. 1021 Pilotopic IIII Pilotopic IIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIIII		· · · · · · · · · · · · · · · · · · ·				:					:	:
Auto Nove Nove Nove Nove Nove Nove Nove Nov	Automatic Norma National Triples Tripl	.ongstreet Elem, Add./Renov.				1			:		*	
Geometry Mineson Make State M	General (Websh Mak Shale Mak Shale<	Planning / Bidding	Mon 1/3/05 Fri 9/30/05	1							*	
in february 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	is fixed up 11 Yes reporting	Construction / Move-in	Mon 10/3/05 Thu 8/31/06				1000000				•	•
maximum frinzes ministration	memory Ming fr Mod Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model		فراد المهاري ال	t I		:	Recorden		:		•	:
maximum frinzes ministration	memory Ming fr Mod Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Messarg All My All Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model Mit Mark Mit Messarg Mit Model Mit Model Mit Model	And the second	5-1 314/00			-		:			•	
marry Barly Decustor Wei Steff Wei Steff Wei Steff Marry Steff	marge inform Wei Steff Wei Steff Marge inform							-	·····		:	
description fr 2007 Weir 3004 Based Free 2007 Based Mark 2007 Based <thmark 2007<br="">Based <thmark 2007<br="">Based</thmark></thmark>	description Fr 3000' Ver 3000' <			•	: :	1016105-016-01-01-01-01-01-01-01-01-01-01-01-01-01-		1	:		-	; ;
Construction Ware W Print Store Construction Ware W Print Store Construction Ware W Ware Store Const	Construction Ware No. Project Ware 3000	Planning / Bidding	Wed 1/4/06 Wed 2/28/07	*	: :		the second s				-	
turi Tu turio Tu turio Tu turio turio fasta 1001 fasta 10011 fasta 1001 fast	Gun The fund The fund <ththe fund<="" th=""> The fund T</ththe>	Construction / Move-in	Fri 3/2/07 Wed 12/31/08					PROPERTY AND A CONTRACT OF A DESCRIPTION OF A DESCRIPA DESCRIPTION OF A DESCRIPTION OF A DESCRIPTION OF A DE			i n	
Number No. 1000 No. 1000 <thno. 1000<="" th=""> No. 1000 <t< td=""><td>Number Number Num Num Number</td><td>Demo</td><td>Thu 1/1/09 Fri 5/1/09</td><td>-</td><td>7</td><td><u>.</u></td><td></td><td></td><td></td><td></td><td>2010.00000.0000</td><td>1</td></t<></thno.>	Number Num Num Number	Demo	Thu 1/1/09 Fri 5/1/09	-	7	<u>.</u>					2010.00000.0000	1
Description / Reing Wein (DAG) Fri 122000 Description / Reing Mein (DAG) Fri 227 Description / Reing Mein (DAG) Tra / Prot Meine / Reing Tra / Prot	Description / Reing Wein (DAG) Fit (2008) Description / Reing Wein (DAG) Fit (2008) Description / Reing Wein (DAG) Top / Reing Mering / Reing Wein (DAG) Top / Reing Mering / Reing Top / Reing Top / Reing Top / Reing Mering / Reing Top / Reing Top / Reing Top / Reing Mering / Reing Top / Reing / Reing Top / Reing / Reing Top / Reing			;	1			1 -		10 5 10 10 10 10 10 10 10 10 10 10 10 10 10	-	
Durong Mining Win 1040 Win 1040 Win 1040 Win 1040 Conscient Windows Windows </td <td>Durbarge Wein (1986) Wein (1986) Wein (1986) Wein (1986) Consciention Weinelling Wein (1986) Wein (1986)</td> <td></td> <td>States and the second</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>	Durbarge Wein (1986) Wein (1986) Wein (1986) Wein (1986) Consciention Weinelling Wein (1986)		States and the second									
Contraction Machine Max NUMP Mark NUMP Schwards Filter, Sp. R. Mannar / Benge Contraction / Machine Mark NUMP Mark NUMP Mark NUMP Schwards Filter, Sp. R. Mannar / Benge Contraction / Machine Mark NUMP Mark NUMP Mark NUMP Contraction / Machine Mark NUMP Mark NUMP Mark NUMP Mark NUMP Schwards Filter, Sp. R. Pawel NA. Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP Mark NUMP <td< td=""><td>Contraction Machine Mar 1000 Mar 1000<!--</td--><td></td><td></td><td>2 1 4</td><td></td><td></td><td></td><td></td><td>·····</td><td></td><td>:</td><td>-</td></td></td<>	Contraction Machine Mar 1000 Mar 1000 </td <td></td> <td></td> <td>2 1 4</td> <td></td> <td></td> <td></td> <td></td> <td>·····</td> <td></td> <td>:</td> <td>-</td>			2 1 4					·····		:	-
Construction Week in Lue 1147 Ken 1505 Schwarz Bin Op, JR Ken 1506 File 1000 Schwarz Bin Op, JR Ken 1507 File 1000 Schwarz Bin Ding 15000 File 1000 File 1000 Schwarz Bin Schwarz Bin 15000 File 1000 File 1000 Schwarz Bin Schwarz Bin 15000 File 1000	Consistent Week in Ues 1107 Gen 3000 Consistent Week in Gen 3000 Gen 30000 Gen 30000 Gen 30	Planning / Bidding		:	с	:			:		1	
Same Sen (sp. 9. 8) Sam (sp. 1/2 + 1/10) During (Sn (sp. 1/2 + 1/10) The Sn (sp. 1/2 + 1/10) During (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) Sam (sp. 1/2 + 1/10) Discription (Sn (sp. 1/2 + 1/10) The State (Sn (sp. 1/2 + 1/10)) Discription (Sn (sp. 1/2 + 1/10)) The State (Sn (sp. 1/2 + 1/10)) Discription (Sn (sp. 1/2 + 1/10)) The State (Sn (sp. 1/2 + 1/10)) Discription (Sn (sp. 1/2 + 1/10)) The State (Sn (sp. 1/2 + 1/10)) Discription (Sn (sp. 1/2 + 1/10)) The State (Sn (sp. 1/2 + 1/10)) Discription (Sn (sp. 1/2 + 1/10)) The State (Sn (sp. 1/10)) The State (Sn (sp. 1/10)) Discription (Sn (sp. 1/10)) The State (Sn (sp. 1/10)) The State (Sn (sp. 1/10)) The State (Sn (sp. 1/10)) Discription (Sn (sp. 1/10)) The State (Sn (sp. 1/10)) <ththe (sn="" (sp.="" 1="" 10))<="" state="" th=""> The Sta</ththe>	Same Sen 69, 9 Man (198 Tet 700 Damaged Price No. 100 No. 100 No. 100 Discussion France, Market		Mon 1/1/07 Mon 6/30/08									-
Number 2 Ye 1000 with Ye	Number Name Vacade Standards Name Vacad		(0,1) to $(1,1)$ is a structure to have the distribution of the $(1,1)$ to $(1,1)$. The transmission of the $(1,1)$						A CONTRACTOR OF CONTRACTOR OF CONTRACT	and the second secon	:	
Number 2 Ye 1000 with Ye	Number Name Vacade Standards Name Vacad	ornando Flem Grn RP	Mon 1/2/08 Tus 7/1/08	1							:	
Consumer Wein UKG? The TARS Interprise Team. Mein UKG? The TARS Selection Miners Mein UKG? The Saber Consumer Miners Mein UKG? The Saber Selection Miners The Saber The Saber Selection Miners The Saber The Saber Select	Consumer Went (NAP) The / Mass Interprise (Bass) Went (NAP) 'The / Mass Interprise (Bass) Went (NAP) 'The / Mass Consumer / Mass / Mass 'Went (NAP) 'The / Mass Consumer / Mass / Mass 'Went (NAP) 'Went (NAP) Consumer / Mass / Mass 'Went (NAP) 'Went (NAP) Consumer / Mass / Mass / Mass 'Went (NAP) 'Went (NAP) Consumer / Mass / Ma	· · · · · ·		4	: :	2		karanananananananananananananananananana				1 · ·
Harryste Sinn, Naros, Paradagi (Mating) Contactor Mar 1900 Yes (Mating) Mar 1900 Yes (Ma	Harry Logo Face-spice files. Harrow Face-spice files. Face-spice files. F					8 			:			
State Jack Mon 1200 Yee B300 Springer Binn, Renor, Barning (Monry) Mon 1200 Yee B300 Springer Binn, Renor, Barning (Monry) Mon 1200 Yee B300 Springer Binn, Par, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Springer Binn, Parit / Bur Mon 1200 Mon 1200 Sprin 1200 Mon 1200 Mon	State State State Mon 1200 Yee BSK0 Web 12007 Yee BSK0 Web 12007 State	Construction / Move-in										
Huming Basing Min 1993 This 2008 Granubation Mones Non 1993 This 2008 Second Line Mone, Second Line Mones Non 1993 This 2008 Granubation Mones Non 1993 This 1991 Filt Singer Mones This 1991 This 1991 Granubation Mones This 1991 This 1991 Filt Singer Mones Filt 1992	Impunyi Madang Man. 1930 Man. 1930 Man. 1930 Grandward M. Man. 1930 Man. 1930 Man. 1930 Man. 1930 Segmetar Ellin, Part, Parti Fak. Man. 1930 Man. 1930 Man. 1930 Marana M. Man. 1930 The 1027 The 1028 Man. 1930 Marana M. Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1940 The 1028 Man. 1930 Man. 1930 Man. 1940 The 1028 Man. 1930 Man. 1930 Marana M. Man. 1940 The 1028 Man. 1940 Man. 1940 Man. 1940 The 1028 Man. 1940 Man. 1940 Man. 1940 The 1029 The 1020 Man. 1940 Man. 1940 The 1029 The 1020 Man. 1940 Man. 1940 The 1020 The 1020 Man. 1940 Man. 1940 The 1020 The 1020 Man. 1940 Man. 1940 The 1020 Man. 1940 </td <td></td> <td></td> <td></td> <td>: •</td> <td></td> <td></td> <td>• • • • •</td> <td>:</td> <td></td> <td></td> <td>÷</td>				: •			• • • • •	:			÷
Huming Basing Min 1993 This 2008 Granubation Mones Non 1993 This 2008 Second Line Mone, Second Line Mones Non 1993 This 2008 Granubation Mones Non 1993 This 1991 Filt Singer Mones This 1991 This 1991 Granubation Mones This 1991 This 1991 Filt Singer Mones Filt 1992	Impunyi Madang Man. 1930 Man. 1930 Man. 1930 Grandward M. Man. 1930 Man. 1930 Man. 1930 Man. 1930 Segmetar Ellin, Part, Parti Fak. Man. 1930 Man. 1930 Man. 1930 Marana M. Man. 1930 The 1027 The 1028 Man. 1930 Marana M. Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1930 The 1028 Man. 1930 Man. 1930 Man. 1940 The 1028 Man. 1930 Man. 1930 Man. 1940 The 1028 Man. 1930 Man. 1930 Marana M. Man. 1940 The 1028 Man. 1940 Man. 1940 Man. 1940 The 1028 Man. 1940 Man. 1940 Man. 1940 The 1029 The 1020 Man. 1940 Man. 1940 The 1029 The 1020 Man. 1940 Man. 1940 The 1020 The 1020 Man. 1940 Man. 1940 The 1020 The 1020 Man. 1940 Man. 1940 The 1020 Man. 1940 </td <td>interprise Elem, Renov.</td> <td>Mon 1/2/08 Tue 9/30/06</td> <td>5</td> <td></td> <td></td> <td></td> <td>2</td> <td></td> <td></td> <td></td> <td></td>	interprise Elem, Renov.	Mon 1/2/08 Tue 9/30/06	5				2				
Communication / Marce in Moin (2007) The Stock Signature for Rule, Parel Fak. Moin (2007) Moin (2007) Communication / More in Year (1006) Moin (2007) Communication / More in Year (1006) Communication / More in Moin (2007) Communication / More in Fill (1707) Communication / More in Fill (1707) Communication / More in Fill (1707) Communication / More in	Communication / Marce in Moin 12000 Nue 80005 Signature film Puel, Parel Pael, Nau 11707 Moin 120005 Moin 120005 Communication / More in Yes 11008 Woin 120005 Signature film Pael, Parel Pael, Nau 11707 Yes 11008 Woin 120005 Communication / More in Yes 11008 Woin 120005 Signature film Pael, Pael Pael, Nau 20006 The 120005 Communication / More in Wein 120005 Wrinkle Ellen A Classroom Moin 20005 Paelword More in The 120005 Wrinkle Ellen A Classroom Moin 20005 Paelword More in The 120005 Wrinkle Ellen A Classroom Moin 20005 Paelword More in The 120005 Communication / More in The 1120050 Paelword More in <t< td=""><td>· · · · ·</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>	· · · · ·										
Segment für, Par, Parif Par, Mon 1/07 / Mon 8000 i Pinorg / Seding Mon 1/07 / Mon 8000 i Oranduster / Vinorg Mon 1/07 / Mon 8000 i Discrete / Vinorg / Seding The 1/00 / Parif Vinorg Pinorg / Seding Mon 8000 i Multi & E.A. Addition Pir 61/03 / Parif Vinorg Pinorg / Seding Mon 8000 i Multi & E.A. Addition Pir 61/03 / Parif Vinorg Conductors / Vinorg / Seding Mon 8000 i Multi & E.A. Addition Pin 61/08 / Vinorg Conductors / Vinorg / Seding Mon 8000 i Multi & E.G. Addition / The 1/01/08 / The 1/01/01 The 1/01/08 / The 1/01/01 Pinorg / Seding The 1/01/01 / The 1/01/01	Seguester fürs. Parl, Parui 19.8. Mon 11007 Mon 2006 Pinorg 7 665ng Mon 11007 Mon 2006 Oronautuski 7 (vois 1000 Tus 1000 District R. A. Adlition Pir 1403 Tus 1000 Pinorg 7 665ng Pin 1000 Tus 1000 District R. A. Adlition Pir 1403 Tus 1000 Pinorg 7 665ng Pin 1000 Pin 1000 Conductors 7 (vois 1000 Pin 1000 Must 1000 Pin 1000 Conductors 7 (vois 1000 Pin 1000 Must 1000 Pin 1000 Must 1000 Pin 1000 Must 1000 Pin 1000 Must 1000 Pin 1000 Thus 1000 Pin 1000 Thus 1000 Pin 1000 Must 1000 Pin 1000 Must 1000 Pin 1000 Thus 1000 Pin 1000 Thus 1000 Pin 1000 Thus 1000 Pin 1000 Con	a a construction and a construction of the second		5								
Segivater Elen, Park, Parent Pix, Mon (1/10) Non 60006 Runny (1/10) Non 60006 Construction (1/Norm) The 1010 Runny (1/10) Non 60006 Segivator Elen, Park, Parent Pix, Mon 60006 Malerica K. S. Addition Pri 1/10 Runny (1/10) Non 60006 Construction (1/Norm) Pri 1/10 Runny (1/10) Non 60006 Construction (1/Norm) Pri 1/10 Construction (1/Norm) Non 60006 Construction (1/Norm) The 1/10 Construction (1/Norm) The 1/10 Parenty (1/10) The 1/10 Construction (1/Norm) The 1/10 Parenty (1/10) The 1/10 Construction (1/Norm) The 1/10 Parenty (1/10) The 1/10 Parenty (1/10) The 1/10 Construction (1/Norm) The 1/10 Displant Ellin Parkition Loga The 1/10 Parenty (1/10) The 1/10 Displant Ellin Parkition Loga The 1/10 Parkiting (1/10) The 1/10 Displant Ellin Parkition Loga The 1/10 Parkiting (1/10) The 1/10 Displant Ellin Parkition (1/10) The 1/10 Displant Ellin Parkition (1/10) The 1/10	Segiowater Elem, Park, Parent Pix, Mon 1/100 Mon 60000 Rucing / Lideng Mon 1/007 Man 120107 Construction / Work The 1/00 Mon 60000 Construction / Work The 10010 Construction / Work Mon 60000 Mon 60000 The 10010 Construction / Work Mon 60000 Mon 60000 The 10010 Construction / Work Mon 60000 Mon 60000 The 10010 Construction / Work	CONSCIENT / MOVE-IN		:	я і	x		: : 🛍		rear Annual Contraction of the	:	2
Pielong 1 Mei 1100 1 Mei 120107 Controlleri / Mei 100 1 Tur 10108 Mei 10000 Densitie LA, Addition Parl 40107 The 10108 Pielong / Being Parl 40107 The 10108 Principal Cambridge / Mei 1001 The 10108 Principal Cambridge / Mei 1001 The 10108 Parl 4000 Parl 4000 Parl 4000 The 10108	Pielong 1 Mon (1107) Mon (1107) Mon (1107) Mon (1107) Controllegi / Mon (1107) True (1108) Mon (1107) Mon (1107) Controllegi / Mon (1107) True (1108) Mon (1107) Mon (1107) Palance / Mon (1107) Pielon (1107) True (1107) Mon (1107) Palance / Mon (1107) Pielon (1107) Pielon (1107) Pielon (1107) Palance / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Palance / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (1107) Pielon (1107) Pielon (1107) Policity / Mon (1107) True (11			e 1	: :				÷			
Contraction / Monin Yie 11/00 Her 40005 Alterial FLA Addition Yie 11/00 This 10005 Paratery (Werk) F14 10100 Her 40005 Contraction / Monein Mon 50061 This 10005 Vierificite Elsen A Classroom Mon 50061 This 1050105 Paratery (Work) This 1050105 Contraction / Monein Mon 50061 Werthick Elsen A Classroom Mon 50061 This 1050105 Contraction / Monein This 1050105 Contraction / Monein Madit School FP This 10005 This 10005 Modit School FP This 1000 This 1000 Contraction / Monein This 1000 This 1000 Contraction / Monein / This 10000 This 1000 This 1000 Contraction / Monein / This 10000 This 10000 This 10000 Contraction / Monein / This 100000	Contraction / Moniin Year 1/100 Year 1/100 Altaniii K. A. Addition P1 1/100 Thui 100000 Patalany (K. A. Addition) P1 1/10000 P1 1/100000 Contraction / Mone-In Mare 2008 Thui 100000 Patalany (K. A. Addition) Mare 2008 Thui 100000 Westhelie Elsen A. Classroom Mare 2008 Thui 100000 Patalany (K. Mone-In Thui 100000 Thui 100000 Patalany (K. Mone-In Thui 100000 Thui 100000 Patalany (K. Mone-In Thui 100000 Thui 100000 Construction (Mone-In Thui 100000 Thui 100000 Construction (Mone-In Thui 1000000 Thui 1000000 Construction (Mone-In Thui 10000000 Thui 1000000000000000000000000000000000000	dgewater Elem. Park., Parent Pok.	Mon 1/1/07 Mon 6/30/08					-				
Controction / Workin Yes 1/100 Mon 400001 Attailin K. Addition Yes 1/100 This 10/100 Desting / Mone-in Mon 50.001 This 10/000 Controction / Mone-in Mon 50.001 This 10/000 Operating / Mone-in Mon 50.001 This 10000 Wandride Etern 4 Classroom Mon 50.001 This 10000 Wandride Etern 4 Classroom Mon 50.001 This 10000 Controction / Mone-in Mon 50.001 This 10000 Controction / Mone-in Mon 50.001 This 10000 Wandride Etern 4 Classroom Mon 50.001 This 10000 Wandride Etern 4 Classroom Mon 50.001 This 10000 Wandride School FP This 11/100 This 10000 Construction / Mone-in This 10000 This 100000 Constructin / Mone-in This 1000000 <td>Controction / Workin Yuir 1/100 Mark 00000 Attailin K. Addition P1 0/107 This 10/100 Dealmary / Being Mark 02000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Operating / Being Mon 50,000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being Mon 50,000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being This 10/100 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being This 10/100 This 10/100 Controction / None-in This 10/100 This 10/100 Controction / None-in / This 10/100 This 10/100 This 10/100 Controction / None-in / This 10/100 This 10/100</td> <td>Planning / Bidding</td> <td>Mon 1/1/07 Mon 12/31/07</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>100000000000000000000000000000000000000</td> <td></td> <td>:</td> <td>: :</td>	Controction / Workin Yuir 1/100 Mark 00000 Attailin K. Addition P1 0/107 This 10/100 Dealmary / Being Mark 02000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Operating / Being Mon 50,000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being Mon 50,000 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being This 10/100 This 10/100 Controction / None-in Mon 50,000 This 10/100 Pulsing / Being This 10/100 This 10/100 Controction / None-in This 10/100 This 10/100 Controction / None-in / This 10/100 This 10/100 This 10/100 Controction / None-in / This 10/100 This 10/100	Planning / Bidding	Mon 1/1/07 Mon 12/31/07						100000000000000000000000000000000000000		:	: :
Annalis K. J. Adullion Planney / Biology Planney / Planney / Biology Planney / Biology	Analisis K. A. Adultion Fe 8(100) Fie 9(100) Fiel 9(10		Tue 1/1/08 Mon 6/30/08		: t			in the second seco		****	1	
Petanorg (Biologia) P1 4/107 Tri 10100 Construction, Mow-in Man 34004 Thu 10100 Weinlack (Elsnin 4, Classroom) Mon 53008 Thu 1120100 Petnong (Biologia) Mon 53008 Thu 1120100 Petnong (Biologia) Mon 53008 Weinlack (Elsnin 4, Classroom) Mon 53008 Moni Movi-hi Thu 1108 Thu 1108 Thu 1100 Construction, Movi-hi Thu 1108 Thu 1100 Thu 1100 Planning (Biologia) Thu 1108 Thu 1100 Thu 120100 Construction, Movi-hi Thu 1100 Thu 120100 Thu 120100 Construction, Movi-hi Thu 1100 Thu 120100 Thu 1000 Construction, Movi-hi Thu 1100 Thu 120100 Thu 1000 Deseda Elem ParkBus Loop Thu 1100 Thu 120100 Thu 120100 Construction, Movi-hi Fri 11770 Wein 80010 Thu 11000 Thu 11000 Construction, Movi-hi Thu 11000 Thu 11000 Thu 11000 Thu 11000 Construction, Movi-hi Thu 11000 Thu 11000 Thu 11000 Thu 11000 Construction, Movi-hi Thu 11000 Thu	Petanorg (Biologia) P1 4/107 7 rej 0/108 Construction, Mow-in Mon 9/308 Thu 12/2010 Petanorg (Biologia) Mon 9/308 Thu 12/2010 Petanorg (Biologia) Mon 9/308 Thu 12/2010 Construction, Mox-in Thu 12/2010 Petanorg (Biologia) Thu 12/2010 Construction, Mox-in Thu 12/2010 Construction, Mox-in Thu 12/2010 Construction, Mox-in Thu 12/2010 Petanorg (Biologia) Thu 12/2010 Construction, Mox-in Mon 9/2010 Construction, Mox-in Thu 12/2010 Construction, Mox-in Thu 12/2010 Construction, Mox-in Petanorg (Biologia) Thu 12/2010 Thu 12/2010 Construction, Mox-in Petanorg (Biologia) Construction, Mox-in Thu 12/2010 Construction, Mox-in								1942 1	STAR STREET, STAR	-	
Pearung Biologing Pri of Vor Pri of Vore Construction, Mowa M Mon 3000 Thui 120100 Pearung Biologing Thui 120100 Pearung Biologing Thui 120100 Orishuction / More 3000 Weit 120100 Pearung Biologing Thui 120100 Pearung Biologing Thui 120100 Pearung Biologing Thui 120100 Construction / More An Thui 120100 Pearung Biologing Thui 120100 Construction / More An Thui 120100 Planning Biologing Thui 11000 Thui 120100 Thui 120100 Planning Biologing Thui 11000 Construction / More An Thui 120100 Planning Biologing Thui 11000 Construction / More An Thui 120100 Planning Biologing Thui 120100 Construction / More An Thui 120100 Construction / More An Thui 120100 Constructio	Pearang Bidding Pi # 1/07 Tri pi blicke Construction, Wowsin Man 84/04 Thu 101/05 Weistadde Eleni & Classrooma Mon 530/04 Thu 11/02 Pelaning Bidding Weistadde Eleni & Classrooma Man 84/01 Ocisiuction / Morei-In Thu 11/02 Thu 12/01/06 Planing Bidding Thu 11/02 Thu 12/01/06 Planing Bidding Thu 11/02 Thu 12/01/06 Ocisiuction / Morei-In Thu 11/02 Thu 12/01/06 Planing Bidding Thu 11/02 Thu 12/01/06 Ocisiuction / Morei-In Thu 11/02 Thu 12/01/06 Observal Eleni Pari/Blue Loop Thu 11/02 Thu 12/01/06 Planing / Bidding Thu 11/02 Thu 12/01/06 Observal Eleni Pari/Blue Loop Thu 11/02 Thu 12/01/06 Planing / Bidding Thu 11/02 Thu 11/02 Construction / Morei Fri 11/170 Planing / Bidding Thu 11/02 Construction / Morei Thu 11/02 Thu 11/02 Thu 11/02 Construction / Morei Thu 11/02 Thu 11/02 Thu 11/02		i					: :	:		* *	
Construction / Mae-in Man 840-08 Thú 107/09 Westalde Einh, 4 Classrooma Man 330-08 Thú 107/09 Pinning / Biding Man 330-08 Thú 107/09 Construction / More-in Thú 107/09 Thú 107/09 Mddl, School FF Thú 107/09 Thú 107/09 Pinning / Boding Thú 117/09 Thú 107/09 Mddl, School FF Thú 117/09 Thú 107/09 Pinning / Boding Thú 117/09 Thú 107/09 Pinning / Boding Thú 117/09 Thú 107/09 Pinning / Boding Thú 117/09 Thú 107/09 Construction / More-in Man 14/10 Thú 107/09 Pinning / Boding Thú 117/09 Wed 80010 Pinning / Boding Thú 117/09 Wed 80010 Construction / More-in Fri 117/10 Wed 80010 Construction / More-in Fri 117/10 Wed 80010 Pinning / Boding Thú 117/09 Fri 117/10 Construction / More-in Fri 117/10 Ved 800/10 Pinning / Boding Thú 111/09 Fri 117/10 Constructin / More-in<	Construction / More in Mon 8/008 Thu 10/109 Westalde Einh, 4 Classroom Mon 3/008 Thu 1000 Pinning / Biding Mon 3/008 Thu 1000 Construction / More in Thu 1000 Thu 1000 Pinning / Biding Mon 1/4/10 Thu 1000 Pinning / Biding Mon 1/4/10 Thu 1000 Pinning / Biding Thu 1000 Thu 1000 Pinning / Biding Thu 1000 Thu 1000 Pinning / Biding Thu 1000 Thu 1000 Construction / More in Mon 1/4/10 Thu 6/2011 Construction / More in Thu 1000 Thu 1000 Pinning / Biding Thu 1000 Thu 1000 Construction / More in Fin 1011 Westaldation Construction / More in Fin 10110 Thu 1000 Construction / More in Fin 10110 Thu 1000 Construction / More in Fin 10110 Thu 1000 Construction / More in Fin 10110 Thu 10100 Construction / More in Fin 101100 Fin 101100 Construction / More in <			. 3	±	-		: :				:
Westskide Elem. 4 Classrooms Mon 3300 Thu 1231025 Planning / Bidling Kais School FF Thu 1/100 Thu 1231025 Ontituden / Morie in Mon 3100 Thu 1/100 Thu 1231025 Contraction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/100 Thu 1/2010 Construction / Morie in Mon 3100 Thu 1/2010 Construction / Morie in Morie in Mon 3100 Thu 1/2010 Construction / Morie in Mo	Westslöfe Elen. 4 Clasurooma Planning / Bidding Contructeor / Movie // Planning / Bidding Contructeor / Movie // Planning / Bidding Thu // Movie Planning / Bidding Thu // Movie Construction / Movie Planning / Bidding Thu // Movie Construction / Movie Planning / Bidding Thu // Movie Planning / Bidding / Thu // Movie Planning / Movie Planning / Bidding / Thu // Movie Planning / Movie	Planning / Bidding	Fri 6/1/07 Fri 6/1/08							1		
Warislaide Elam, 4 Classroom Mon 30309 Thui 120109 Planning / Bidding Mon 30309 Thui 120109 Constluction / Morein Thui 120109 Thui 120109 Models School FF Thui 120109 Thui 20109 Planning / Boding Thui 120109 Thui 20109 Constluction / Morein Thui 120109 Thui 20109 Planning / Boding Thui 120109 Thui 20109 Constluction / Morein Mon 12010 Thui 20110 Constluction / Morein Mon 12010 Thui 20110 Observalue Elam Parkibus Loop Thui 1100 Thui 120100 Constluction / Merein Fri 11100 Weet 80010 Planning / Bidding Thui 1100 Thui 1100 Constluction / Merein Fri 11100 Thui 1100 Planning / Bidding Thui 1100 Thui 1100 Constluction / Merein Fri 11100 Tue 1120100 Constluction / Merein Fri 11100 Tue 1120100 Constluction / Merein Fri 11100 Tue 112010 Planning / Bidding Thui 1100 Fri 11210	Warislake Elam, 4 Classroom Planning Bläding Contituden / More S1009 Thu 120109 Contituden / More S1009 Thu 120109 Thu 1		Mon 6/4/08 Thu 10/1/09						:			-
Planning / Blading Work 12/31/05 Construction / Movie/in Thu 17/03 Thu 17/03 Thu 12/31/05 Planning / Blading Thu 11/04 Diamong / Blading Thu 11/05 Thu 11/05 Thu 12/31/05 Construction / Movie/in Won 15/1/10 Construction / Movie/in Won 15/1/10 Construction / Movie/in Won 15/1/05 Construction / Movie/in Won 15/1/05 Construction / Movie/in Won 15/1/05 Construction / Movie/in Fin 11/1/05 Planning / Blading Thu 11/1/05 Thu 11/105 Thu 12/31/05 Construction / Movie/in Fin 11/1/05 Planning / Blading Thu 11/105 Thu 11/105 Thu 11/105 Thu 11/105 Thu 11/105 Planning / Blading Thu 11/105 Planning / Blading <t< td=""><td>Planning / Blading Monishing Thu 17/03 Thu 12/03 Construction / Monishin Thu 17/03 Thu 12/03 Planning / Blading Thu 11/04 Thu 12/04 Planning / Blading Thu 11/05 Thu 12/04 Construction / Monishin Moni 14/10 Thu 12/04 Construction / Monishin Moni 14/10 Thu 12/04 Planning / Blading Thu 11/03 Thu 12/04 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading / Blading Thu 11/05 Thu 12/01 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading / Blading Thu 11/05 Thu 12/02 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading Thu 11/05 Thu 12/02 Planning / Blading Thu 12/02 Thu 12/02</td><td>er marine er er</td><td></td><td></td><td>: :</td><td>1</td><td></td><td>1 -</td><td></td><td>Tradition of the second se</td><td>· · · · · · · · · · · · · · · · · · ·</td><td></td></t<>	Planning / Blading Monishing Thu 17/03 Thu 12/03 Construction / Monishin Thu 17/03 Thu 12/03 Planning / Blading Thu 11/04 Thu 12/04 Planning / Blading Thu 11/05 Thu 12/04 Construction / Monishin Moni 14/10 Thu 12/04 Construction / Monishin Moni 14/10 Thu 12/04 Planning / Blading Thu 11/03 Thu 12/04 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading / Blading Thu 11/05 Thu 12/01 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading / Blading Thu 11/05 Thu 12/02 Construction / Monishin Fin 11/10 Wed 8/20/10 Planning / Blading Thu 11/05 Thu 12/02 Planning / Blading Thu 12/02 Thu 12/02	er marine er			: :	1		1 -		Tradition of the second se	· · · · · · · · · · · · · · · · · · ·	
Planning / Blaiding Monitory / Blaiding Models 61:00 PF Thu 11/10 ²⁰ Thu 12/23:009 Thu 11/10 ²⁰ Thu 12/23:009 Planning / Blaiding Thu 11/10 ²⁰ Thu 12/23:009 Image: State Stat	Planning / Blaiding Monitory / Blaiding Monitory / Blaiding Monitory / Blaiding Thu 11/109 Thu 12/2010 Thu 12/2010 Thu 12/2010 Describe Effer Thu 11/109 Wed 800/10 Thu 12/2010 Describe Elem. Media, Classman. Thu 11/109 Wed 800/10 Thu 12/2010 Describe Elem. Media, Classman. Thu 11/109 Thu 11/109 Thu 12/2010 Describe Elem. Media, Classman. Thu 11/109 Thu 11/109 Thu 11/109 Planning / Blaiding Thu 11/109 Thu 11/109 Thu 11/109 Describe Elem. Media, Classman. Thu 11/109 Thu 11/109 Thu 11/109 Planning / Blaiding Thu 11/109 Thu 11/109 Thu 11/109 Planning / Blaiding Thu 11/109 Thu 11/109 Thu 11/109 Describe Elem. Media, Classman. Thu 11/101 Thu 11/1010 Thu 11/101 Thu 11/1010	Nortelda Elam A Ciannagura	No- 3/3/08 Thu 10/31/00	1		а ж				×	1	
Construction / Moix-in Thu 1/1/02 Thu 1/2/03/02 Middle School FF Thu 1/1/02 Thu 1/1/02 Planning / Bidding Thu 1/1/02 Fil 1/1/02 Construction / Mov-in Men 1/2/10 Thu 1/1/02 Planning / Bidding Thu 1/1/02 Wed 8/30/10 Construction / Mov-in Fil 1/1/02 Wed 8/30/10 Planning / Bidding Thu 1/1/02 Thu 1/1/02 Construction / Mov-in Fil 1/1/02 Wed 8/30/10 Planning / Bidding Thu 1/1/02 Thu 1/1/02 Construction / Mov-in Fil 1/1/02 Wed 8/30/10 Planning / Bidding Thu 1/1/02 Fil 1/1/02 Construction / Mov-in Fil 1/1/02 Fil 1/1/02 Docetol Elem. Media, Classman. Thu 1/1/02 Fil 1/1/10 Planning / Bidding Thu 1/1/02 Fil 1/1/10 Docetol Elem. Vindeg Tue 1/1/2/10 Fil 1/1/10 Planning / Bidding Tue 1/1/2/10 Fil 1/1/10 Docetol Elem. Vindeg Tue 2/1/11 Fil 1/1/10 Docetol Elem. Vindeg Tue 2/1/11 Fil 1/1/10 Docetol Elem. Ungd. Heno. Tue 2/1/11 Fil 1/1/10 </td <td>Construction / Moix-in Thu 1/1/03 Thu 1/201/05 Middle School FF Thu 1/1/09 Fil 1/1/0 Planning / Bloding Thu 1/1/09 Fil 1/1/0 Construction / Mov-in Mon 1/2/10 Thu 1/1/09 Objected Elem Park/Bus Loop Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Construction / Mov-in Fil 1/1/0 Thu 1/201/06 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Thu 1/1/09 Construction / Mov-in Fil 1/1/10 Planning / Bloding Thu 1/1/09 Scoolar Elem. Neidla, Classman. Thu 1/1/09 Planning / Bloding Thu 1/1/09 Scoolar Elem. View in Fil 1/1/10 Scoolar Elem. View in Thu 1/1/09 Scoolar Elem. View in Thu 1/1/09 Planning / Bloding Thu 1/1/09 Scoolar Elem. Vieg / 1/11 Thu 1/1/09 Planning / Bloding Tus 1/1/10 Planning / Bloding Tus 1/1/10 Planning / Bloding Tus 1/1/</td> <td></td> <td></td> <td></td> <td></td> <td>5 2</td> <td></td> <td></td> <td></td> <td></td> <td><u>.</u></td> <td></td>	Construction / Moix-in Thu 1/1/03 Thu 1/201/05 Middle School FF Thu 1/1/09 Fil 1/1/0 Planning / Bloding Thu 1/1/09 Fil 1/1/0 Construction / Mov-in Mon 1/2/10 Thu 1/1/09 Objected Elem Park/Bus Loop Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Construction / Mov-in Fil 1/1/0 Thu 1/201/06 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Weet 6X0/10 Planning / Bloding Thu 1/1/09 Thu 1/1/09 Construction / Mov-in Fil 1/1/10 Planning / Bloding Thu 1/1/09 Scoolar Elem. Neidla, Classman. Thu 1/1/09 Planning / Bloding Thu 1/1/09 Scoolar Elem. View in Fil 1/1/10 Scoolar Elem. View in Thu 1/1/09 Scoolar Elem. View in Thu 1/1/09 Planning / Bloding Thu 1/1/09 Scoolar Elem. Vieg / 1/11 Thu 1/1/09 Planning / Bloding Tus 1/1/10 Planning / Bloding Tus 1/1/10 Planning / Bloding Tus 1/1/					5 2					<u>.</u>	
Middle School FF Thu 11/1/09 Thu 92/11 Construction / More in Mon 14/10 Thu 92/11 Decessor International Construction / More in Fri 11/1/09 Wed 9/20/10 Planning / Bidding Thu 12/20/00 Construction / More in Fri 11/1/09 Wed 9/20/10 Construction / More in Fri 11/1/09 Thu 12/20/00 Planning / Bidding Thu 12/20/00 Construction / More in Fri 11/1/09 Thu 12/20/00 Planning / Bidding Thu 1/20/00 Planning / Bidding Thu 2/20/10 Planning / Bidd	Middle School FF Thu 11/1/09 Thu 82/11 Construction / More in Planning / Bidding Thu 11/1/09 Thu 92/11 December 2010 Thu 11/1/09 Thu 92/11 December 2010 Dec	· · · · · · · · · · · · · · · · · · ·				1		: :	:		Contract of the second s	
Planning / Bidding Thu 1///09 Fri 1///10 Construction / Movein Mon 1/4/10 Thu 62/71 Descela Elem Park/Bus Loop Thu 1/1/09 Wed 40/30/10 Planning / Bidding Thu 1/1/09 Wed 40/30/10 Construction / Movein Fri 1/1/10 Wed 60/30/10 Planning / Bidding Thu 1/1/09 Thu 1/2/31/09 Construction / Movein Fri 1/1/10 Wed 60/30/10 Dissocial Elem. Media, Chavarma. Thu 1/2/31/0 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Dissocial Elem. Media, Chavarma. Thu 1/2/10 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Dissocial Elem. Upgal, Eleo. Tue 2/1/10 Planning / Bidding Tue 2/1/10 Dissocial Elem. Upgal, Eleo. Tue 9/1/09 Tue 9/1/09 Tue 9/1/09	Planning / Bidding Thu 11/109 Fri 11/110 Construction / Move-in Mon 1/4/10 Thu 5/2/11 Descela Elem Park/Bus Loop Thu 11/109 Wed 8/30/10 Planning / Bidding Thu 11/109 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/1/10 Wed 8/30/10 Construction / Move-in Fri 11/1/10 Wed 8/30/10 Disclosed Elem. Media, Chavarma. Thu 11/2/10 Planning / Bidding Thu 2/1/10 Construction / Move-in Mon 11/4/10 Tue 9/1/00 Tue 9/1/10 Construction / Move-in Tue 9/1/	Construction / Move-In	Thu 1/1/09 Thu 12/31/09	1	: :	;		· · · · · · ·	;			
Planning / Bidding Thu 1///09 Fri 1///10 Construction / Movein Mon 1/4/10 Thu 62/71 Descela Elem Park/Bus Loop Thu 1/1/09 Wed 40/30/10 Planning / Bidding Thu 1/1/09 Wed 40/30/10 Construction / Movein Fri 1/1/10 Wed 60/30/10 Planning / Bidding Thu 1/1/09 Thu 1/2/31/09 Construction / Movein Fri 1/1/10 Wed 60/30/10 Dissocial Elem. Media, Chavarma. Thu 1/2/31/0 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Dissocial Elem. Media, Chavarma. Thu 1/2/10 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Planning / Bidding Thu 1/2/10 Dissocial Elem. Upgal, Eleo. Tue 2/1/10 Planning / Bidding Tue 2/1/10 Dissocial Elem. Upgal, Eleo. Tue 9/1/09 Tue 9/1/09 Tue 9/1/09	Planning / Bidding Thu 11/109 Fri 11/110 Construction / Move-in Mon 1/4/10 Thu 5/2/11 Descela Elem Park/Bus Loop Thu 11/109 Wed 8/30/10 Planning / Bidding Thu 11/109 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/110 Wed 8/30/10 Construction / Move-in Fri 11/1/10 Wed 8/30/10 Construction / Move-in Fri 11/1/10 Wed 8/30/10 Disclosed Elem. Media, Chavarma. Thu 11/2/10 Planning / Bidding Thu 2/1/10 Construction / Move-in Mon 11/4/10 Tue 9/1/00 Tue 9/1/10 Construction / Move-in Tue 9/1/	to be a set of the second of the second s	···· ·································	1							1	
Planning / Bidding Thu 1//09 Fil 1//10 Construction / Move-in Mon 1///0 Thu 6/2/11 Obsecta Elem Park/Bus Loop Thu 1//09 Wed 4/30/10 Planning / Bidding Thu 1//09 Wed 4/30/10 Planning / Bidding Thu 1//109 Wed 6/30/10 Construction / Move-in Fil 1//10 Fil 1//10 Planning / Bidding Thu 1//2/0 Fil 1//10 Planning / Bidding Thu 1//2/0 Fil 1//10 Construction / Move-in Mon 1///10 Tue 1//2/0 Planning / Bidding Tue 9//00 Tue 2/1/11 Planning / Bidding Tue 9//00 Tue 9//00 Planning / Bidding Tue 9//00 Tue 9//00	Planning / Budding Thu 1/1/09 Fri 1/1/10 Construction / More-in Mori 1/4/10 Thu 6/2/11 Obsecta Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Bidding Thu 1/1/09 Thu 1/1/09 Construction / More-in Fri 1/1/10 Construction / More-in Fri 1/1/10 Construction / More-in Fri 1/1/10 Planning / Bidding Thu 1/1/09 Construction / More-in Fri 1/1/10 Planning / Bidding Thu 1/1/108 Construction / More-in Fri 1/1/10 Planning / Bidding Thu 1/1/09 Planning / Bidding Thu 1/1/08 Planning / Bidding Thu 1/1/10 Planning / Bidding Thu 1/1/08 Planning / Bidding Tue 9/1/09 Tue 9/1/09 Tue 9/1/09 Tue 9/1/09 Tue 9/1/09	Alddie School FF	Thu 1/1/09 Thu 5/2/11	•							` <u> </u>	
Construction / Move-in Mon 1/4/10 Thu 6/2/11 Sociala Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Bidding Thu 1/1/09 Thu 1/2/10 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Sociala Elem, Media, Classrma. Thu 1/1/09 Tue 11/2/10 Planning / Bidding Thu 1/1/09 Fri 1/1/10 Sociala Elem, Media, Classrma. Thu 1/1/09 Fri 1/1/10 Planning / Bidding Thu 1/1/09 Fri 1/1/10 Sociala Elem, Media, Classrma. Thu 1/1/09 Fri 1/1/10 Planning / Bidding Thu 1/1/09 Tue 1/1/2/10 Sociala Elem, Upgd, Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 9/1/09 Tue 2/1/11	Construction / Move-in Mon 1/4/10 Thu 6/2/11 Sociala Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Bidding Thu 1/1/09 Wed 6/30/10 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Construction / Move-in Fri 1/1/10 Construction / Move-in Fri 1/1/10 Construction / Move-in Fri 1/1/10 Planning / Bidding Thu 1/1/09 Planning / Bidding Thu 1/1/10 Sociala Elem. Media, Classrms. Thu 1/1/10 Planning / Bidding Thu 1/1/10 Sociala Elem. Upgd, Eleo. Tue 9/1/09 Sociala Elem. Upgd, Eleo. Tue 9/1/09 Planning / Bidding Tue 9/1/09				t 1	-		: .			-	h :
Deceola Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Blading Thu 1/1/09 Thu 12/21/09 Construction / Move-in Fit 11/1/10 Wed 6/30/10 Planning / Blading Thu 1/1/09 Tue 11/2/10 Deceola Elem. Upgd, Elec. Tue 9/1/09 Tue 21//11 Planning / Blading Tue 9/1/09 Tue 21//11	Dsceola Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Blading Thu 1/1/09 Thu 12/31/09 Construction / Move-in Fit 11/1/10 Wed 6/30/10 Planning / Blading Thu 11/20/10 Planning / Blading Tue 91/09 Tue 21//11 Planning / Blading Tue 91/09 Tue 21//11										And the second	
Doseola Elem Park/Bus Loop Thu 1/1/09 Wed 6/30/10 Planning / Bidding Thu 1/1/09 Thu 12/31/09 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Chisholm Elem, Media, Classrma, Thu 1/1/08 Tue 11/2/10 Planning / Bidding Thu 1/1/08 Fri 1/1/10 Construction / Move-in Move-in Move-in Tue 11/2/10 Planning / Bidding Tue 2/1/11 Planning / Bidding Tue 2/1/11 Planning / Bidding Tue 2/1/11	Doseola Elem Park/Bus Loop Thu 1/1/09 Wed 8/30/10 Planning / Bidding Thu 1/1/09 Thu 12/21/09 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Chisholm Elem, Media, Classrma, Thu 1/1/08 Tue 11/2/10 Planning / Bidding Thu 1/1/08 Fri 1/1/1/0 Construction / Move-in Move-in Move-in Tue 11/2/10 Planning / Bidding Tue 1/1/2/10 Doseola Elem. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 9/1/09 Tue 2/1/11	CONCERNING MARCHIN						:	÷		:	and the second
Planning / Blidding Thu 1/1/09 Thu 1/1/09 Thu 1/1/09 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Chisholm Elem, Media, Classrme. Thu 1/1/08 Tue 11/2/10 Planning / Blidding Thu 1/1/09 Tue 11/2/10 Construction / Move-in Mon i///10 Tue 11/2/10 Obsecola Elem, Upgd, Eleo. Tue 2/1/11 Planning / Blidding Tue 2/1/10 Construction / Move-in Tue 2/1/10 Construction / Move-in Tue 2/1/11 Elem. Upgd, Eleo. Tue 2/1/11 Planning / Blidding Tue 2/1/10	Planning / Blidding Thu 1/1/09 Thu 1/1/09 Thu 1/1/09 Construction / Move-in Fri 1/1/10 Wed 6/30/10 Chisholm Elem, Media, Classrme. Thu 1/1/08 Tue 11/2/10 Planning / Blidding Thu 1/1/09 Tue 11/2/10 Construction / Move-in Mon 1/4/10 Tue 11/2/10 Planning / Blidding Tue 11/2/10 Obsecola Elem. Upgd. Eleo. Tue 2/1/11 Planning / Blidding Tue 2/1/10 Construction / Move-in Tue 2/1/10 Planning / Blidding Tue 2/1/10 Planning / Blidding Tue 2/1/10	1 A.		;	:			: :	1		1	-
Construction / Nove-In Fri 1/1/10 Wed 6/30/10 Shisholm Elem, Media, Classrms. Thu 1/1/08 Tue 11/2/10 Planing / Bidding Thu 1/1/09 Fri 1/1/10 Construction / Nove-In Moni 1/4/10 Tue 11/2/10 Science Elem, Upgd, Eleo. Tue 9/1/09 Tue 2/1/11 Planing / Bidding Tue 9/1/09 Tue 2/1/11	Construction / Nove-In Fit 1/1/10 Wed 6/30/10 Shisholm Elem, Media, Classrms, Thu 1/1/03 Tue 11/2/10 Planning / Bidding Thu 1/1/03 Fit 1/1/10 Construction / Move-In Moni 1/4/10 Tue 11/2/10 Science Elem, Upgd, Eleo, Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 9/1/09 Tue 2/1/11	Sceola Elem Park/Bus Loop	Thu 1/1/09 Wed 8/30/10				*				1000000000	
Construction / Nove-in Fri 1/1/10 Wed 6/30/10 Chisholm Elem, Media, Classrme. Thu 1/1/08 Tue 11/2/10 Planning / Bildung Thu 1/1/08 Fri 1/1/10 Construction / Move-in Moni 1/4/10 Tue 11/2/10 Obseiola Elem. Upgd. Eleo. Tue 9/109 Tue 2/1/11 Planning / Bildung Tue 9/109 Tue 2/1/11	Construction / Nove-in Fit 11/1/0 Wed 6/30/10 Chisholm Elem, Media, Classrme. Thu 11/108 Tue 11/2/10 Planning / Bildung Thu 11/2/10 Fit 11/1/10 Construction / Move-in Moni 11/2/10 Obsecola Elem. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bildung Tue 9/1/09 Tue 2/1/11	Planning / Bidding	Thu 1/1/09 Thu 12/31/09									n :
Chisholm Elem. Medla, Classrms. Tue 11/2/10 Planning / Bidding Thu 1/1/08 Construction / Move-in Mon 1/4/10 Construction / Move-in Mon 1/4/10 Scenala Elem. Upgd. Eleo. Tue 9/1/09 Planning / Bidding Tue 9/1/09 Planning / Bidding Tue 9/1/09 Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 6/1/09	Chisholm Elem. Medla, Classrms. Thu 11/203 Tue 11/2/10 Planning / Bidding Thu 11/203 Fri 11/1/10 Construction / Move-In Mon 1/4/10 Tue 11/2/10 Discoola Elem. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 9/1/09 Tue 2/1/11			1				•	:			1
Planining / Bildding Thu (1/1/29) Fri 1/1/10 Construction / Move-in Mon (1/4/10) Tue 1/1/2/10 Discerola Elem. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planining / Bildding Tue 9/1/09 Tue 6/1/10	Planining / Bildding Thu (1/1/29) Fril 1/1/10 Construction / Move-In Mon (1/4/10) Tue 1/1/2/10 Disceptial Elem. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bildding Tue 9/1/09 Tue 6/1/100	and the second s				*		:				Second Second State
Planining / Bidding Thu (1/103) Fri (1/1/10) Construction / Move-In Mon (1/4/10) Tue 1/1/2/10 Sociola Elem. Upgd. Eleo. Tue 9/1/09) Tue 2/1/11 Planning / Bidding Tue 9/1/09) Tue 6/1/100	Planining / Bildding Thu 1/1/03 Fri 1/1/1/0 Construction / Move-In Mon 1/4/10 Tue 1/1/2/10 Sociola Elem. Upgd. Eleo. Tue 9/1/03 Tue 2/1/11 Planning / Bildding Tue 9/1/03 Tue 6/1/10	1 9 1 10 10 10 10 10 10 10 10 10 10 10 10 1		*	: 1	1	•					
Construction / More-In Mon 1/4/10 Tue 11/2/10 Sociola Elem. Upgd. Eleo. Tue 3/1/09 Tue 2/1/11 Plánning / Bidding Tue 3/1/09 Tue 6/1/10	Construction / More-In Mon 1/4/10 Tue 11/2/10 Sociola Elem. Upgd. Eleo. Tue 3/1/09 Tue 2/1/11 Planning / Bidding Tue 3/1/09 Tue 6/1/10						1					
Construction / More-In Mon 1/4/10 Tue 11/2/10 Sociola Elem. Upgd. Eleo. Tue 3/1/09 Tue 2/1/11 Plánning / Bidding Tue 3/1/09 Tue 6/1/10	Construction / More-In Mon 1/4/10 Tue 11/2/10 Sociola Elem. Upgd. Eleo. Tue 3/1/09 Tue 2/1/11 Planning / Bidding Tue 3/1/09 Tue 6/1/10							: :	:		101000000000000000000000000000000000000	1 :
Disceola Elem. Upgd. Eleo. Tue 3/1/09 Tue 2/1/11 Planning / Bidding Tue 3/1/09 Tue 6/1/10	Disceola Elen. Upgd. Eleo. Tue 9/1/09 Tue 2/1/11 Planning / Bidding Tue 9/1/09 Tue 6/1/10		Mon 1/4/10 Tue 11/2/10		: · · · · ·	:	2 • ·	1	:			
Planning / Bidding Tue 9/1/09 Tue 6/1/10	Planning / Bidding Tue 9/1/09 Tue 6/1/10					-		:	:			AND A REPORT OF A
Planning / Bidding Tue 9/1/09 ¹ Tue 6/1/10	Planning / Bildding Tue 9/1/09 ¹ Tue 6/1/10	ting and the second states and the second st	T				1	:	:			
						- - -	•		:			
	Construction / Move-In Wed 6/2/10 Tue 2/1/11				: :	:	5 1	;	: ;			
Construction / Move-in Wed 6/2/10 Tue 2/1/11		Construction / Move-in	Wed 6/2/10 Tue 2/1/11		1 A		•		-			

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0)

				NCA - Not currently										
	bea an introdu		-	MOST RECENT	ORIGINAL PROJECT	CHANGES IN				(NON-SALES TAX) OTHER	TOTAL SALES	TOTAL COST	- 1941 - 1940	
AME	DESCRIPTION	Last Revision - 1 NEW SCHOOLS	IO/YR	ESTIMATE	ESTIMATE	SCOPE	CONTINGENCY	INFLATION	TOTAL	FUNDS	TAX FUNDS	TO DATE	UNCOMMITTED	COMMENTS / NOTES
New Elementary "V"	South Halifax			NCA	11,000,000	0	0	0	11,000,000	0	11,000,000	0	11.000.000	Site search has begun.
New Elementary "W"	Southwest Volusia		05/03	10,294,180	11,000,000	287,075	(2,013,013)	1,020,118	10,294,180	75	10,294,105	8,692,948		Construction started 5/15/03.
New Elementary "X"	Southwest Volusia		05/03	12,212,255	11,000,000	810,900	(649,506)	1,050,861	12,212,255	0	12,212,255	740,426	11,471,829	In design and permitting. To bid August 200
New Elementary "Y" New Elementary "Z"				NCA	11,000,000	0	0	0	11,000,000	0	11,000,000	0	11,000,000	
New cleanealitary 2."				NCA	11,000,000	0	. 0	0	11,000,000	0	11,000,000	0 -	11,000,000	
New Middle School "DD"	Southwest Volusia			NCA	20,000,000	575,413	0	0	20,575,413	575,413	20,000,000	575,413	20,000,000	
New Middle School "FF"	Southeast Volusia			NCA	20,000,000	668,586	0	0	20,668,586	668,361	20,000,225	668,586	20,000,000	
New Middle School "GG"	North Halifax		05/03	22,017,097	20,000,000	1,200,092	(1,093,652)	1,910,657	22,017,097	993,918	21,023,179	19,302,823	2,714,274	Contract awarded. Const. started June 2003
New High School "DDD"	West Volusia			NCA	40,000,000	25,102	0	0	40,025,102	0	40,025,102	164,435	39.860.667	Two sites under option.
											10,020,102			
	EXISTING	ELEMENTARY SCHOOLS										×		
Blue Lake Elementary	Renovations: HVAC rep classrooms and up-grad	lacement, ceiling and lightin le interior finishes.	9	NCA	735,000	0	0	0	735,000	0	735,000	7,672	727,328	
Bonner Elementary	Site work: provide additi	onal parking and develop		NCA	2,690,000	0	0	0	2,690,000	0	2,690,000	3,300	2,686,700	
		I. Renovations: remove Bldg	. 6											
	up-grade HVAC campus 10 classrooms.	s wide. New construction:												
Chishoim Elementary	Renovations: HVAC up-	grade campus wide. New		NCA	1,700,000	0	0	0	1,700,000	0	1,700,000	305,917	1 394 083	HVAC started
•	construction: media cen media to 3 resource roo	ter. Remodeling: existing ms.				_		-	.,		.,			
Coronado Elementary		HVAC and electric service lets, exterior wall systems		NCA	813,000	0	0	0	813,000	· 0	813,000	149,984	663,016	Kitchen HVAC is complete
Edgewater Elementary	Site work: pave parent p additional parking	blck-up drive and provide		NCA	250,000	0	0	0	250,000	0	250,000	. 0	250,000	
Enterprise Elementary	Develop courtyard and	nt pick-up loop, remove Bldg provide ext. lighting. New Ition, P.E. and material stora ghting in media center		NCA	2,605,000	0	0	0	2,605,000	o	2,605,000	. 0	2,605,000	
Hurst Elementary	Replacement	- -		NCA	11,000,000	0	0	0	11,000,000	0	11,000,000	0	11,000.000	
Longstreet Elementary	Renovations: classroom	windows and doors, group		NCA	1,650,000	0	0	. 0	1,650,000	0	1,650,000	0	1,650,000	
		al up-grade campus wide				·	·		1,000,000		1,000,000	-	1,000,000	
Geo. Marks Elementary		classroom finishes and cabi npus wide electrical up-grad		NCA	1,660,000	0	0	0	1,660,000	0	1,660,000	0	1,660,000	
Ormond Beach Elementary	Site expansion		05/03	269,567	200,000	77,019	(7,452)	0	269,567	77,019	192,548	263,207	6,360	Two additional parcel purchased
Ortona Elementary	New construction: admi Renovation: exterior wai up-grade electrical syste	Is campus-wide and		NCA	925,000	0	0	0	925,000	o	925,000	70,808	854,192	Walls complete in phase I Elect. in planning-Construction Summer 200

•

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0)

			0	ORIGINAL		•			(NON-SALES			_	
AME	DESCRIPTION Last Revision	MO/YR ESTIN	ECENT P		CHANGES IN SCOPE	CONTINGENCY	INFLATION	TOTAL		TOTAL SALES	TOTAL COST	UNCOMMITTED	COMMENTS / NOTES
Osceola Elementary	Site expansion, improve bus loop and provide additional parking. Renovations: up-grade electric service campus wide.	NO		470,000	0	0	0	470,000	0	470,000	0	470,000	
Plerson Elementary	Site work: remove fuel island, develop playground provide parent pick-up loop. Renovations: campus wide electrical up-grade. New construction: remov Bldgs. 14 & 16 and construct new art room, stora guidance and two resource rooms.	e l	CA .	1,943,000	0	0	Ō	1,943,000	0	1,943,000	0	1,943,000	
Port Orange Elementary	HVAC up-grade campus-wide	NC	XA	200,000	0	0	0	200,000	o	200,000	33,900	166,100	Design 80% complete
Read-Pattillo Elementary	Renovations: exterior windows and doors Expand site	NC	A	460,000	0	0	0	460,000	0	460,000	0	460,000	
TT Small Elementary	New construction cafeteria. Remodel: existing food service to music room, and Bldg. 08 to art ro		796,486	1,500,000	152,652	69,196	74,638	1,796,486	152,652	1,643,834	1,811,812	(15,326)	Project complete.
South Daytona Elementary	Renovations: Up-grade HVAC campus wide. Site work: provide additional paved parking, remove Bl and 3. New construction: 12 classrooms and expa food service.		A	4,458,412	0	0	0	4,458,412	O	4,458,412	69,892	4,388,520	Survey & solls complete, in planning,
Sunrise Elementary	Connect to city sewer	NC	A	200,000	0	0	0	200,000	o	200,000	0	200,000	
Tomoka Elementary	Renovations: restrooms in classroom pods, exteri wall systems, Site work: covered walkway to parent pick-up.	or NC	A	315,000	0	0	0	315,000	O	315,000	48,500	266,500	In planning, Design 75% complete
Volusia Pines Elementary	New construction: eight classroom addition	05/03 1,288	,522	2,175,000	0	(1,060,257)	173,779	1,288,522	o	1,288,522	1,188,523	99,999	Under construction.
Westside Elementary	New construction: 2 classroom and 2 resource	NC	A	650,000	0	0	0	650,000	o	650,000	0	650,000	
	EXISTING MIDDLE SCHOOLS												
Campbell Middle	Replacement facility	05/03 26,216	6,185 2	20,000,000	26,216,185	(20,000,000)	0	26,216,185	26,216,185	0	24,191,915	2,024,270	Construction to be complete Aug. 2003
DeLand Middle	A/C gymnasium	NC	A	500,000	0	0	0	500,000	o	500,000	72,020	427,980	In permitting
Galaxy Middle	Remodel 6th grade science rooms	NC	A	500,000	0	0	0	500,000	o	500,000	2,708	497,292	In design and planning
Holly Hill Middle	Master plan campus	NC	XA 2	20,000,000	0	0	0	20,000,000	0	20,000,000	_ 0	20,000,000	
New Smyma Beach Middle	Site work: improve drainage between bldgs. Renovations: Air condition kitchen	NC	A	500,000	0	0	0	500,000	0	500,000	24,642	475,358	Survey and borings complete. AC is bidd
Ormond Beach Middle	Master Plan	NC	CA 1	10,000,000	0	0	0	10,000,000	o	10,000,000	0	10,000,000	
Southwestern Middle	Renovations: gym a/c, locker rooms and windows convert shop in Bldg. 04 to technology lab, campu wide electrical up-grade. Site work: provide paren drop-off and pick-up loop.	IS	CA .	1,620,000	0	0	0	1,620,000	O	1,620,000	737,623	882,377	In design. Site work complete.
	EXISTING HIGH SCHOOLS												

.

30

.

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0)

				NCA - Not currently										
NAME.	DESCRIPTION	Last Revision - M	10/YR	MOST RECENT ESTIMATE	ORIGINAL PROJECT ESTIMATE	CHANGES IN SCOPE	CONTINGENCY	INFLATION	TOTAL	(NON-SALES TAX) OTHER FUNDS	TOTAL SALES	TOTAL COST	UNCOMMITTED	COMMENTS / NOTES
Atlantic High	New construction, 8 cirms, 3			NCA	3,525,000	0	0	0	3,525,000	0	3,525,000	0	3,525,000	
DeLand High	Phase 3 Master Plan		05/03	27,217,610	15,600,000	5,941,661	4,239,922	1,436,027	27,217,610	5,941,661	21,275,949	24,630,849	2,586,761	Auditorium & renovations under const.
Deltona High	Renovations: provide A/C in and food labs. Site work: res		6/03	10,651,243	1,975,000	7,952,013	534,395	189,835	10,651,243	7,952,013	2,699,230	1,067,514	9,583,729	Costs represents HVAC complete campus. Only unalrcondition space funded by Sales Tax, Under construction.
Mainland High	Master Plan		05/03	52,599,521	40,000,000	3,790,289	4,911,198	3,898,034	52,599,521	2,666,546	49,932,975	50,402,546	2,196,975	Construction started May 2003.
New Smyrna Beach High	Replacement facility		05/03	47,345,048	40,000,000	3,007,509	121,446	4,216,093	47, 34 5,048	58,728	47,286,320	4,380,216	42,964,832	Plans received to bid July 2003 Project to start Sept. 2003
Seabreeze High	Master Plan Phase III		05/03	8,803,129	7,000,000	1,243,024	147,773	412,332	8,803,129	1,243,024	7,560,105	8,700,722	102,407	Project complete.
Spruce Creek High	New construction: media cen Remodeling: existing media t		oms	NCA	8,185,000	0	0	0	8,185,000	0	8,185,000	2,164,846	6,020,154	In design and planning. Setting temp campus.
T.D. Taylor Middle/High	Master Plan		05/03	29,198,012	20,000,000	409,893	6,520,824	2,267,295	29,198,012	60,655	29,137,357	1,995,218	27,202,7 9 4	In design.
	DIST	RICT WIDE												
Elementary Campuses	New and replacement playgr Covered play area (pavilions)			NCA	3,960,000	55,419	0	0	4,015,419	55,419	3,960,000	1,073,454	2,941,965	22 schools complete for playground equip.
Alternative Education	Southwest Southeast Euclid		05/03	2,401,350 NCA NCA	3,000,000 3,000,000 2,000,000	0 0 0	(841,304) 0 0	242,654 0 0	2,401,350 3,000,000 2,000,000	0 0 0	2,401,350 3,000,000 2,000,000	1,604,865 0 0	796,485 3,000,000 2,000,000	Site with building under contract.
	1	OTALS		252,310,205	392,964,412	52,412,832	(9,120,430)	16,892,323	453,149,137	46,661,669	406,487,468	155,147,284	298,001,853	
		· · ·				IGINAL REP	ORT	200.004.452		**		*** * Cao #?hc====	e la Sanna ^{ll} Denort	- /T-chall
		1		TOTAL CONSTRUC	HON COST			392,964,412 33.035.588				*	s in Scope" Report as in Scope" Report	(LOtal) (Non-Sales Tax Funds)
				SUBTOTAL				426,000,000				-	apital Management	LINE STOP LALL OFMS
				CONSTRUCTION IN	FLATION AND IN	TEREST ON DE	BT	89,000,000						
				TOTAL AVAILABLE				(54,000,000)						

NCA - Not currently available

.

SALES TAX PROJECTS STATUS REPORT AS OF June 30, 2003 <u>CHANGES IN SCOPE</u> <u>ASSUMPTIONS AND EXPLANATIONS</u>

FUTURE NON-SALES TAX FUNDS: A funding source (other than Sales Tax Funds) may have to be found for a part of a Sales Tax Project's cost. As these funds are encumbered they will be reclassified to NON-SALES TAX FUNDS (See below).

NON-SALES TAX FUNDS: Funds encumbered or expended from sources other than Sales Tax Funds.

LAND PURCHASES WITH SALES TAX FUNDS: Sales Tax Funds were originally intended to be used for only the construction parts of a Sales Tax Project excluding land purchases and off-site development cost. These amounts have or will be encumbered and expended for land purchases of the Sales Tax Project.

<u>OFF-SITE COST PAID WITH SALES TAX FUNDS</u>: Sales Tax Funds were originally intended to be used for only the construction parts of a Sales Tax Project excluding land purchases and off-site development cost. These amounts have or will be encumbered and expended for off-site development.

TOTAL: Total CHANGES IN SCOPE for a Sales Tax Project. Represents the sum of FUTURE NON-SALES TAX FUNDS + NON-SALES TAX FUNDS + LAND PURCHASES WITH SALES TAX FUNDS + OFF-SITE COST PAID WITH SALES TAX FUNDS.

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0) Changes in Scope

					Changes In Sco	pe		
1.17			Future Non- Sales	Non- Sales Tax	Land Purchased with	Off-Site Costs Paid With Sales Tax		
AME	DESCRIPTION	Last Revision - MO/YR V SCHOOLS	Tax Funds	Funds	Sales tax Funds	Funds	Total	Comments / Notes
	(45\$)	SCHOOLS						-
New Elementary "V"	South Halifax		0	. 0	0	0	•	
New Elementary "W"	Southwest Volusia	05/03	0	75	0		0	,
	Southwest Volusia	1	0		•	287,000	287,075	
New Elementary "X"	Southwest volusia	05/03	0	. 0	35,900	775,000	810,900	
New Elementary "Y"			0	0	0	0	0	
New Elementary "Z"			0	0	0	0	0	
New Middle School "DD"	Southwest Volusia		0	575,413	0	0	575,413	
New Middle School "FF"	Southeast Volusia		0	668,361	225	0	668,586	
New Middle School "GG"	North Halifax	05/03	0	993,918	6,174	200,000	1,200,092	
						· · ·		
New High School "DDD"	West Volusia		0	0	25,102	0	25,102	
						· · · ·		
	EXISTING ELE	MENTARY SCHOOLS						
Blue Lake Elementary	Renovations: HVAC replacer	ment, ceiling and lighting	0	. 0	0	0	0	
	classrooms and up-grade int		• /	•	Ũ	0	v	
Sonner Elementary	Site work: provide additional	parking and develop	0	0	0	0	0	
Dominical Electrication y	kindergarten playground. Re		U	U	0	0	0	
	up-grade HVAC campus wid	le. New construction:						
	10 classrooms.							
	D			_				
Chisholm Elementary	Renovations: HVAC up-grad		0	0	0	0	0	,
•	construction: media center. F	Remodeling: existing						
	media to 3 resource rooms.							
Coronado Elementary	Renovations: up-grade HVA	C and electric service	0	0	0	0	0	
	campus-wide, group toilets,	exterior wall systems						
		-						
Edgewater Elementary	Site work: pave parent pick-u	up drive and provide	0	0	0	0	0	
	additional parking			•	•	0	•	
Enterprise Elementary	Site work: provide parent pic	k-up loop remove Bldg 08	0	0	0	0	0	
encopros clontencery	Develop courtyard and provid		v	Ŭ	0	0	U	
	construction: administration,							
	Renovation: up-grade lighting	y in media center						
lunt florenter :	Destingenerat		-		-	-	-	
Hurst Elementary	Replacement	4	0	0	0	0	0	
		,		<u>,</u>				
Longstreet Elementary	Renovations: classroom wind		0	0	0	0	0	
	tollets (student), electrical up							
	New construction: music and	d art rooms						
Geo. Marks Elementary	Renovations: up-grade class		0	0	0	0	0	
	HVAC replacement, campus	wide electrical up-grade						
Ormond Beach Elementary	Site expansion	05/03	0	77,019	0	0	77,019	
*					-	-		
Ortona Elementary	New construction: administra	ation/quidance.	0	0	0	0	0	
	Renovation: exterior walls ca		Ŭ			v	v	
	up-grade electrical system c				, · ·	· · · · ·	- · · · · · ·	
	grace acoulou oyotoin o							
Osceola Elementary	Site expansion, improve bus	loon and provide	0	0	•	0	^	
Carrona mana italy			U	U	0	0	0	
	additional parking. Renovation	nos un arodo ologiciani						

33

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0) Changes In Scope

					Changes in Sco	ha		
			Fiture Non Sales	Non-Soles Ter	I and Durahand with	Off-Site Costs Paid		
IAME	DESCRIPTION	Last Revision - MO/YR	Future Non- Sales Tax Funds	Non- Sales Tax Funds	Land Purchased with Sales tax Funds	With Sales Tax Funds	Total	Commente / Notes
	service campus wide.			runo	Callis Lax Funds	runas	Iotal	Comments / Notes
	·							
Pierson Elementary	Site work: remove fuel isla	and develop playeround	0	0				
Fielson crementery	provide parent pick-up loop		0	U	0	. 0	0	
	wide electrical up-grade. N							
	Bldgs. 14 & 16 and constru	uct new art room, storage,						
	guidance and two resource	e rooms.		·				
Port Orange Elementary	HVAC up-grade campus-v	vide	0	0	0	0	0	
				-	-		v	
Read-Pattillo Elementary	Renovations: exterior wind	dows and doors	0	0	0	. O .	· 0	
	Expand site							
TT Small Elementary	New construction cafeteria	a, Remodel: existing 05/03	0	152,652	0	0	152,652	
	food service to music room	n, and Bldg. 08 to art room		•				
South Daytona Elementary	Renovations: Up-grade HV	AC compus wide Site	0	. 0	0	^		
South Daytond Elementary	work: provide additional pa	aved parking, remove Bldgs 2	0	, U	U	0	0	
	and 3. New construction: 1							
	food service.							
Sunrise Elementary	Connect to city sewer		0	0	0	0	0	
·····,				Ŭ	Ŭ	. •	Ū	
Tomoka Elementary	Renovations: restrooms in		0	0	0	0	0	
	wall systems, Site work: c	covered walkway to						
	parent pick-up.							
Volusia Pines Elementary	New construction: eight cla	assroom addition 05/03	0	0	0	0	0	
181	N		_		_			·
Westside Elementary	New construction: 2 classr	room and 2 resource	. 0	0	0	0	0	
	EXISTING	MIDDLE SCHOOLS						
Campbell Middle	Replacement facility	05/03	2,024,270	24,191,915	0	0	26,216,185	Project is being totally funded by COPS funds.
					-	·		
DeLand Middle	A/C gymnasium		0	0	0	0	0	
Galaxy Middle	Remodel 6th grade science	e rooms	0	0	0	0	0	
	-							
Holfy Hill Middle	Master plan campus		0	0	0	0	Ó	
New Smyrna Beach Middle	Site work: improve drainag	je between bidgs.	0		0	0	0	
•	Renovations: Air condition			Ŭ	· ·	v	0	
0	Mantas Dias			-		_		A. Contraction of the second se
Ormond Beach Middle	Master Plan		0	0	0	0	0	
Southwestern Middle	Renovations: gym a/c, locl		0	0	0	0	0	
	convert shop in Bldg. 04 to							
	wide electrical up-grade. S							
	drop-off and pick-up loop.							
	EXISTIN	IG HIGH SCHOOLS				to a construction of the		
			1					
Atlantic High	New construction, 8 clrms	3 science 2 voc. labs	0	0	0	0	0	

SALES TAX PROJECTS STATUS REPORT AS OF JUNE 30, 2003 (\$0) Changes In Scope

		· · · · · · · · · · · · · · · · · · ·				Off-Site Costs Paid		
			Future Non- Sales	Non- Sales Tax	Land Purchased with	With Sales Tax		
IAME	DESCRIPTION	Last Revision - MO/YR	Tax Funds	Funds	Sales tax Funds	Funds	Total	Comments / Notes
DeLand High	Phase 3 Master Plan	05/03		5,941,661	<u>Sales tax r unus</u>	<u> </u>	<u>5,941,661</u>	
Decand high	Fildse 5 Waster Fidit	00/03	l v	5,541,001	. 0	Ŭ	5,941,001	
Deltona High	Renovations: provide A/C in	n gymnasium, kitchen, 06/03	7,660,814	291,199	0	0	7.952.013	Future non-sales tax funds will be from a COPS issue.
	and food labs. Site work: re						1. 1	
Mainland High	Master Plan	05/03	1,250,000	1,416,546	973,743	150,000	3,790,289	Vince Carter funding \$2,500,000 of gym \$1,250,000 has been received.
					<u>.</u>			
New Smyrma Beach High	Replacement facility	05/03	0	58,728	2,688,781	260,000	3,007,509	Was COPS, now Sales Tax for land purchase.
Seabreeze High	Master Plan Phase III	05/03	0	1,243,024	0	0	1,243,024	
Seableeze righ		00/03	, v	1,243,024	Ű		1,243,024	
Spruce Creek High	New construction: media co	enter and 20 new classrooms	0	0	0	0	0	
-p	Remodeling: existing media		_				-	
T.D. Taylor Middle/High	Master Plan	05/03	0	60,655	349,238	0 -	409,893	
								,
	DIS	TRICT WIDE						
Elementary Campuses	New and replacement plays	around equipmont	0	55,419	0	0	55,419	
Elementary Campuses	Covered play area (pavilion			55,419	Ū	Ũ	55,415	
	Covered play area (parment							
Alternative Education	Southwest	05/03	0	0	0	0	0	
	Southeast		0	0	0	0	0	
	Euclid		0	0	. 0	0	0	
			10.005.004	05 700 505	4 070 400	4 070 000	FO 440 000	
		TOTALS	10,935,084	35,726,585	4,079,163	1,672,000	52,412,832	
•			TOTAL NON-SALES TAX >	46,661,669			•	
				**				
				* Soo "SALES TAY PD	OJECTS STATUS" Report (NO	ONLEATES TAX OTHER FU	NDS	
					ROJECTS STATUS" Report (C			
					Concerent and Address			

35
